


2015 FEDERAL CONSTITUENCY PROJECTS



LESSONS AND FINDINGS FROM FOCUS STATES

www.tracka.ng

16 FOCUS STATES (2015 CONSTITUENCY PROJECTS)

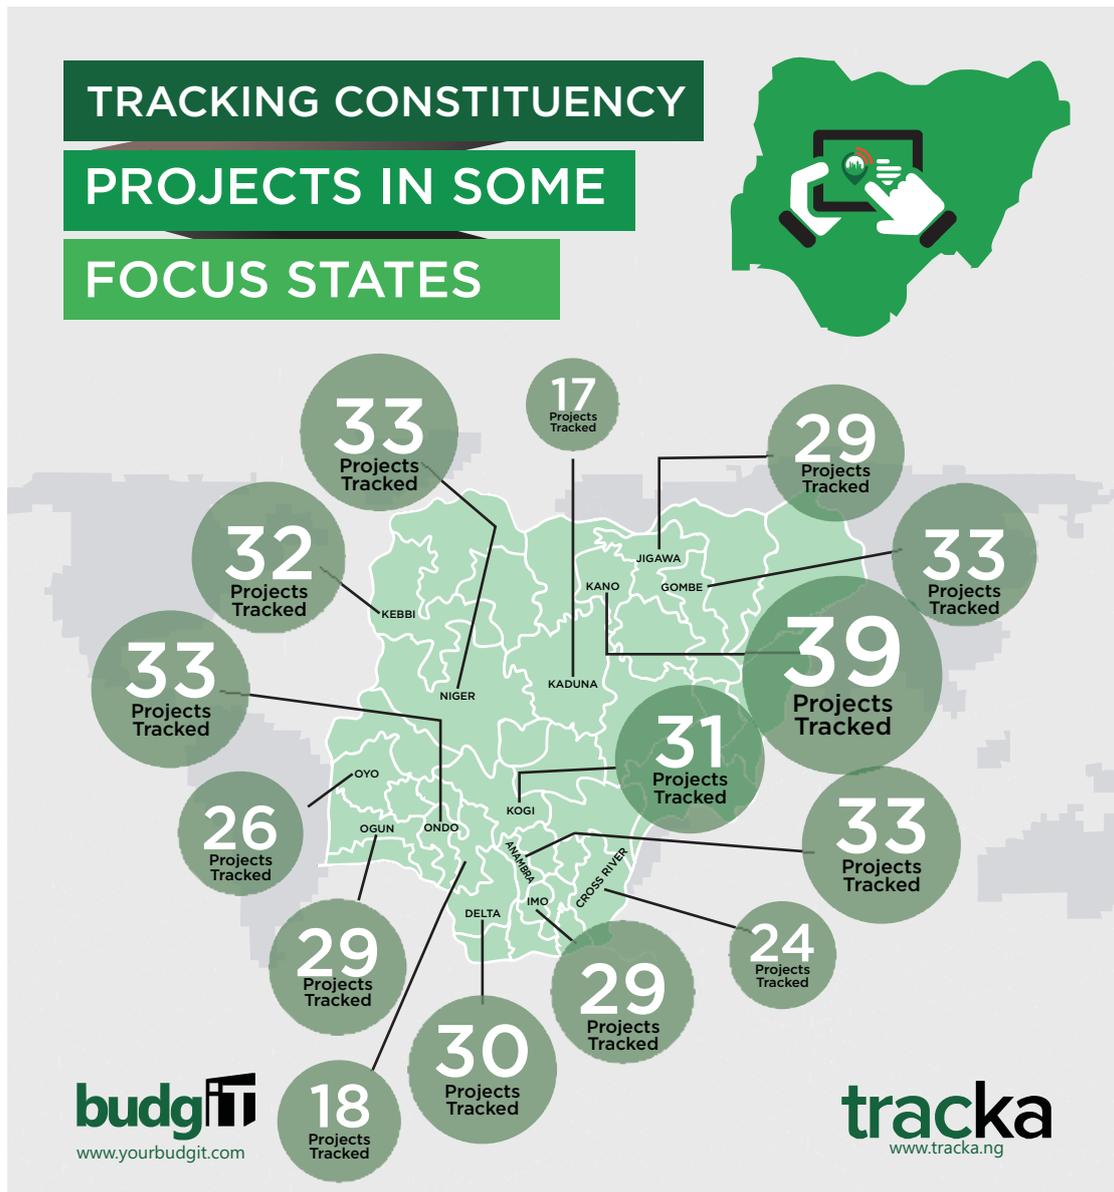

Tracka seeks to address a lack of access of citizens to the information of budget formulation and execution in Nigeria; it aims to empower citizens to demand transparency and accountability in the Nigerian government. The project kicked off with 16 States of the Federation, namely- Kogi, Ogun, Oyo, Kano, Edo, Delta, Anambra, Kaduna, Niger, Gombe, Lagos, Ondo, Imo, Cross River, Kebbi, and Jigawa.

There are Project Tracking Officers to monitor the progress of constituency projects across the 16 focus states, exploring the use of technology to track budgets and also report feedbacks to the related executive and legislative bodies.

INTRODUCTION

Citizen-government engagement in Nigeria remains at abysmally low levels due to vestiges of past military rule, in which autocratic regimes kept the populace in obscurity about data and acts of public governance.

Democracy, widely known as “government of the people, by the people and for the people,” is persistently mainly beneficial to those in power. To enjoy the true dividends of democracy, citizens must hold governments accountable and demand a presence in all aspects of decision-making at local, State and federal level, a presence that is legally enforced, not solely constitutionally-backed.

Tracka was created to assist active interested citizens in efficiently tracking budgets and public projects in their respective communities. The reoccurrence of capital projects listed and not executed in successive budget dampens the spirit of people whose sense of belonging comes from an inclusion in the State and Federal budgets. The platform is therefore layered on Open Data, bringing people aware of their civic duties together to share photos, videos, documents and also post comments on existing projects, and alert government and civil society to the non-implementation of any capital projects as well.

As a social platform, Tracka enables citizens to monitor capital projects such as roads, schools, hospitals, boreholes and street lights, in their neighbourhoods, with accompanying SMS integration to enable the grassroots stay connected without a smartphone. Tracka is citizen-driven, kickstarting and sustaining discussions around public projects whilst simultaneously facilitating feedback to all relevant public offices and officers.

Within Tracka, budget line items are simplified and developed into interactive applications, visuals, and infographics - to enhance citizens' understanding, and shared, using social media tools to enhance debate centred on national and subnational budgets. Project locations are geo-tagged, to ensure unimpeachable accuracy and encourage inputs from other residents in similar region, ostensibly providing multiple streams of corroboration.

Offline, regular townhall meetings are held to engage the grassroots, utilising cell groups formation to sensitize communities about the specific budget line items that warrant public scrutiny to ensure optimal responses from government. With an interactive website and mobile-friendly application, Tracka is primarily built to widen citizen knowledge about budget priorities and empower digitally-literate Nigerians to collaborate for efficient service delivery.

This project addresses an endemic lack of access to information on budget formulation and execution in Nigeria; as a tool Tracka seeks to stimulate a public appetite for Open Data, access to budgetary information and increased performance monitoring, which will subsequently promote inclusive growth and sustainable development in the federal constituencies that make up Africa's most populous nation.

NIGER STATE

NO. OF PROJECTS TRACKED	COMPLETED	ONGOING	NOT DONE
33	4	5	24



SAMPLE PROJECTS

Project: Provision of 60 hand pump boreholes to rural communities in Gurara, Suleja, and Tafa LGA
Cost: N68 million

This project leads the three other water provision schemes which have not been implemented. We report pervasive inflation of the costs for water and empowerment programs in the State, with projects largely uncompleted in its communities.

Residents of these areas still lack basic amenities, particularly water, and they are subjected to the hardship of traveling miles to fetch potable water. In addition to the previous sum allocated for water supply, there was an additional N10 million awarded for the completion of solar-powered boreholes in Ijah Gbayi and Bonu in Gurara, Suleja, and Tafa constituencies. This has been completed, although the water station was out of service as at the time of our last confirmation visit in February 2015.



Borehole at Ijah Gbah

Project: Solar Powered Borehole in Ijah Gbah

Cost: N10 million

Mr. Barnabas Daudu, the Principal of Community School, Ijah Gbayi, expressed their disappointment over this borehole, and said: "It didn't even work up to one month; the pumping machine stopped working and couldn't run water to the overhead tank."

One of the Millennium Development goals (MDGs) in the 2015 budget allocated N40 million for the provision of 20 hand-pump boreholes, at N2 million each for the Niger East Senatorial District. So far, this project has been impossible to track, as there are no location details to enable PTOs pin-point the relevant communities.

Project: Supporting poverty eradication through economic empowerment projects and skill acquisition in Gurara,

Suleja, and Tafa Federal Constituency, Niger State

Cost: N300 million

Our designated PTO met with the community heads to discuss the program's status; unfortunately, the people were not aware of the provision for these schemes in the budget. This project is the most significant in terms of costs, and leads a list of four other empowerment programs currently uncompleted in the State.

Project: Construction of Clinic at Garafini, Borgu LGA

Cost: N3.60 million

Although completed, this clinic can barely serve basic healthcare provision purposes. The facility can only accommodate two beds at a time, and is therefore grossly inadequate for the community which has at least hundreds of residents.



Clinic at Garafini, Borgu LGA

MINISTRY	AGENCY	ITEMS	AMOUNT	STATUS	OBSERVATION
LANDS	LANDS	UPGRADING OF FACILITIES INCLUDING CONSTRUCTION OF LECTURE HALLS, LABORATORY AND WATER SUPPLY/ ELECTRICITY SUPPLY, ETC, IN THE CAMPUS OF NIGER STATE UNIVERSITY/ COLLEGE OF EDUCATION SULEJA, NIGER STATE	36,000,000	ONGOING	PROJECT IS ONGOING AS AT TIME OF VISIT
HEALTH	NPHCDA	COMPLETION AND EQUIPPING OF 3 NO. PRIMARY HEALTH CENTRES AT GAWUN BABABNGIDA, TUNA AND BABBAN TUNGA IN GURARA/SULEJA/TAFE FEDERAL CONSTITUENCY, NIGER STATE	55,000,000	NOT DONE	NO INDICATION OF THE PROJECT ON SIGHT EXCEPT FOR AN UNCOMPLETED BUILDING IN TUNA CONSTITUENCY, NIGER.
POWER	NREA	ELECTRIFICATION OF DAUPE, APO, GAURAKA, TOBA, CHIPO, ZIDNA AND CHAWA (TAFE LGA), TUNGAN TSAUNI, NUMBA TUKURA, PADAMAN ABUCHI AND KWANKASHE EXTENSION (SULEJA LGA); AND ABUCHI GWALE, BURUM, TUCHI, LAHU, GUSUN, PASALI, TAILE, LONDNA, DAGIBE, AND T/WADA, BOYI & DADO, (GURARA LGA) IN GURARA/SULEJA/TAFE FEDERAL CONSTITUENCY, NIGER STATE	90,000,000	NOT DONE	GAURAKA, TUNGA TSAUNI, NUMBS TUKURA AND CHAWA HAVE BEEN ELECTRIFIED OVER SEVEN YEARS AGO, THE OTHER COMMUNITIES LISTED DO NOT HAVE ACCESS TO POWER.
WATER	UNRBDA	PROVISION OF 60 NOS. HANDPUMP BOREHOLES TO RURAL COMMUNITIES IN GURARA/SULEJA/TAFE LGA, NIGER STATE	68,000,000	NOT DONE	MOST OF THE COMMUNITIES VISITED IN THE LG LACK BOREHOLES AND FOR OTHERS THE BOREHOLES ARE NOT FUNCTIONAL AND REQUIRE REPLACEMENTS.
WORKS	FERMA	REHABILITATION OF BWARI-GARAM-WUSE LINK ROAD TO ABUJA- KADUNA EXPRESSWAY	83,000,000	NOT DONE	THE LAST REHABILITATION WAS DONE TWO YEARS AGO AND THE ROAD IS NOW IN A DEPLORABLE STATE.
SGF	REFUGEES	PROVISION OF EDUCATIONAL SUPPORT/GRANTS TO STUDENTS OF TERTIARY AND NON-TERTIARY INSTITUTIONS INCLUDING PAYMENTS OF EXAMINATION FEES IN GURARA/SULEJA/TAFE FEDERAL CONSTITUENCY, NIGER STATE	50,000,000	NOT DONE	NON OF THE RESIDENTS WERE AWARE OR COULD ATTEST TO THE PROGRAM IN THE THREE LOCAL GOVERNMENTS
SGF	REFUGEES	SUPPORTING POVERTY ERADICATION THROUGH ECONOMIC EMPOWERMENT PROJECTS AND SKILL ACQUISITION IN GURARA/SULEJA/TAFE FEDERAL CONSTITUENCY, NIGER STATE	300,000,000	NOT DONE	NON OF THE RESIDENTS WERE AWARE OR COULD ATTEST TO THE PROGRAM IN THE THREE LOCAL GOVERNMENTS
SCIENCE	ECN	COMPLETION OF SOLAR POWERED BOREHOLES IN IJAH GBAYI AND BONU IN GURARA/SULEJA/TAFE FEDERAL CONSTITUENCY, NIGER STATE	10,000,000	DONE	BOREHOLE HAS BEEN SUPPLIED TO IJAH GWARI BUT IT IS NON FUNCTIONAL. NO BOREHOLE IN BONU.
EDUCATION	UBEC	PROVISION OF EXERCISE BOOKS AND INSTRUCTION MATERIALS IN GURARA/SULEJA/TAFE FEDERAL CONSTITUENCY, NIGER STATE	8,000,000	ONGOING	ONGOING IN SOME SCHOOLS WHILE OTHERS ARE WAITING FOR THEIR PROVISIONS.
WOMEN	NCWD	SUPPLY OF KEKE NAPEP AT MINNA/ CHANCHAGA FEDERAL CONSTITUENCY	30,000,000	DONE	MEMBERS OF THE COMMUNITY EXPRESSED HOW HELPFUL THE PROVISION HAS BEEN TO THE COMMUNITIES.
TRADE	SMEDAN	STRATEGIC EMPOWERMENT, ENTERPRISE CREATION AND DEVELOPMENT AT AGAIE/LAPAI	42,000,000	NOT DONE	NON OF THE RESIDENTS WERE AWARE OR COULD ATTEST TO THE PROGRAM IN THE TWO LOCAL GOVERNMENTS
TRADE	SMEDAN	SKILL ACQUISITION AND YOUTH EMPOWERMENT; SUPPLY OF TRICYCLES, MOTORCYCLES, SEWING MACHINES FOR LAVUM, EDAH & MOKWA FED. CONSTITUENCY	50,000,000	NOT DONE	MATERIALS HAVE BEEN SUPPLIED TO EDATI BUT COMMUNITY MEMBERS ARE YET TO SEE THE MATERIALS.
LABOUR	NDE	SUPPLY OF TRICYCLE MACHINE AT BOSSO/PAIKORO LGA NIGER STATE	37,500,000	NOT DONE	RESIDENTS WERE NOT AWARE AND COULD NOT VERIFY PROGRAM IN THE TWO LOCAL GOVERNMENTS
EDUCATION	UBEC	CONSTRUCTION OF 4 NOS BLOCKS OF 3 NOS BLOCKS OF 3 CLASSROOMS AT TUCHI, BURU, LAHU AND ABUCHI VILLAGE COMMUNITIES IN GURARA/SULEJA/TAFE FED.CONST.	37,500,000	ONGOING	PROJECT IS ONGOING IN ALL THE COMMUNITIES EXCEPT LAHU. WE OBSERVED 1 BLOCK CLASSROOM BUILDINGS AT TUCHI, BURU & ABUCHI.

MINISTRY	AGENCY	ITEMS	AMOUNT	STATUS	OBSERVATION
SGF	REFUGEE	EMPOWERMENT IN CHANCHANGA IN FEDERAL CONSTITUENCY, MINNA . SUPPLY OF TRICYCLES AND MOTORCYCLES	18,750,000	DONE	TRICYCLES HAVE BEEN SUPPLIED AND DISTRIBUTED TO COMMUNITY MEMBERS
TRADE	SMEDAN	SKILLS ACQUISITION IN CHACHANGA FED. CONSTITUENCY, MINNA NIGER STATE: SUPPLY OF FREEZERS, SOWING, GRINDING MACHINES	18,750,000	DONE	MATERIALS HAVE BEEN SUPPLIED AND DISTRIBUTED TO COMMUNIITY MEMBERS.
EDUCATION	UBEC	PURCHASE OF TOYOTA HIACE 2.7LTR FOR CHECHE SEC. SCHOOL, KATCHA LGA. NIGER STATE	8,000,000	NOT DONE	CONSIDERING THE DISTANCE OF THE COMMUNITY TO THE SCHOOL LOCATED IN A REMOTE AREA, THE BUS WILL EASE THE MOVEMENT OF STUDENTS IN THE COMMUNITY.
EDUCATION	UBEC	GENERAL RENOVATION AND FURNISHING OF OLD CLASSES AT CHECHE PRY SCH, KATCHA LGA	10,000,000	NOT DONE	THE LAST RENOVATION AND FURNISHING WAS DONE IN 2013.
EDUCATION	UBEC	CONSTRUCTION OF POLICE OUTPOST AND FURNISHING AT CHECHE, KATCHA LGA	8,000,000	NOT DONE	THE POLICE OUT POSE IN THE COMMUNITY IS CAVING IN AND THERE ARE NO POLICE AT THE STATION.
EDUCATION	UBEC	ICT TRAINING FOR STUDENT OF GOVERNMENT DAY SEC SCH CHECHE, KATCHA LGA	22,000,000	DONE	TRAINING HAS BEEN COMPLETED FOR TEACHERS AND STUDENTS AND COMPUTERS WERE SUPPLIED TO THE SCHOOL.
EDUCATION	NECO	NOV/DEC NECO EXAMINATION AT GOVERNMENT DAY SEC. SCH CHECHE, KATCHA LGA	2,000,000	DONE	THE FURNITURE WERE SUPPLIED AND THE SCHOOL WAS USED AS THE EXAM CENTER
WATER	UNRBDA	CONSTRUCTION OF 5 NOS HANDPUMP BOREHOLE AT BORGU LGA	6,306,306	NOT DONE	RESIDENTS COULD NOT VERIFY BOREHOLE SUPPLIES TO THE LOCAL GOVERNMENT AREA
WATER	UNRBDA	CONSTRUCTION OF CLINIC AT GARAFINI, BORGU LGA	3,603,604	DONE	THE CLINIC IS BELOW STANDARD AND TOO SMALL TO ATTEND TO MORE THAN TWO ADMISSIONS AT A TIME.
WATER	UNRBDA	CONSTRUCTION OF CLINIC AT GARAFINI, BORGU LGA	3,603,604	DONE	COMPLETED, ALTHOUGH INDIGENES COMPLAIN THE NEW MOSQUE IS SMALLER THAN THE CENTRAL MOSQUE OF THE COMMUNITY.
WATER	UNRBDA	CONSTRUCTION OF MULTI PURPOSE HALL, NEW BUSSA LGA	900,901	NOT DONE	PROJECT HAS NOT BEEN IMPLEMENTED
WATER	UNRBDA	ELECTRIFICATION OF KURWASA ,BORNU LGA	2,252,252	NOT DONE	THE POLES HAVE BEEN MOUNTED WITHOUT CABLES, THE COMMUNITY STILL LACK ACCESS TO POWER.
TRADE	SMEDAN	2 NOS 500/11 KVA TRANSFORMERS AT NEW BUSSA	7,207,207	NOT DONE	PROJECT HAS NOT BEEN IMPLEMENTED
		6 NOS SOLAR STREET LIGHT AT NEW BUSSA	4,504,505	NOT DONE	PROJECT HAS NOT BEEN IMPLEMENTED
WATER	UNRBDA	ELECTRIFICATION OF GARAFINI	1,351,351	NOT DONE	THE POLES IN SIGHT WERE MOUNTED YEARS AGO BY THE WORLD BANK WITHOUT CABLES, THE COMMUNITY STILL LACK ACCESS TO POWER.
WATER	UNRBDA	CONSTRUCTION OF 6NOS HANDPUMP BOREHOLE IN BORGU LGA	7,567,568	NOT DONE	PROJECT HAS NOT BEEN IMPLEMENTED
WATER	UNRBDA	CONSTRUCTION OF BRIDGE AT MONAI, BORGU LGA	5,495,495	NOT DONE	THE BRIDGE AT THE COMMUNITY IS FALLING APART.

ANAMBRA STATE

NO. OF PROJECTS TRACKED	COMPLETED	ONGOING	NOT DONE
33	15	14	4

tracka
www.tracka.ng

SAMPLE PROJECTS

PROJECT: Procurement of 13 pieces of Kia Saloon Car at N5mn each for Women Empowerment in Anaocha LGA, Anambra State

Cost: N65 million

Field reports indicate this project does not have direct impact on the women in Anambra. Project does not have a direct impact on the women in Anaocha LGA and is also highly prone to fraud.

In sum, seven other empowerment programs in the 2015 Anambra constituency budgets are noted as difficult to track with regards to implementation as there are scant details to enable monitoring, making the likelihood of misappropriation of funds higher. The programs are:

1. Supply of 11 Commercial Taxi for Economic Empowerment in Idemili North & South LGA - N45 million
2. Supply of 35 Tricycles for Economic Empowerment in Idemili North &



Ihiala Township Stadium

- South LGA - N25 million
3. Supply of 16 Motorcycles for Economic Empowerment in Idemili North & South LGA - N5 million
 4. Supply of 600 Units of Sewing Machines and Supply of 300 Units of Motorcycles in Ogbaru Constituency - N40 million
 5. Supply of Generator Sets and Deep Freezers in Ogbaru Constituency - N10 million
 6. Supply of Sewing Machines and Industrial Cloth Weaving Machine in Ayamelum/Oyi Constituency - N50 million
 7. Strategic Empowerment Programme in Ihiala LGA - N28 million

PROJECT: Training and reinstatement of members of Orumba Farmers Cooperative Society in Orumba North/South Federal Constituency

COST: N20 Million

Prior to monitoring visits by PTOs, community members were unaware of the provision for this project in the budget. This project remains unimplemented, and the Farmers cooperative society in Orumba report that they have not received any form of support from the government.

The reinstatement scheme is a laudable one, as if delivered, it will strengthen the farmers' working strategies, ultimately boosting food production from the community and raising household income rates. Constituents are however concerned about its implementation and the lack of transparency which has ensured they remain in the dark about the scheme.

PROJECT: Construction of a Block of 3 Classrooms with VIP Toilets at Umuchu, Aguata LGA, Anambra State

COST: N14 million

Tracka's PTOs visited the Umuchu community repeatedly and report that there was nothing in sight at the project location; construction work as at the time of monitoring is noted as nonexistent.

Our engagement with the pupils and teachers revealed that the entire community lacks large classrooms or a hall that can accommodate students for general examinations.

There are several provisions for school buildings in Anambra. However, most of them require an access road to the school location. The deplorable conditions of access roads affect the movement of commuters on a daily basis, likely contributing to a stagnancy of the education sector; residents and community heads implore the government to look into the situation.

PROJECT: Rehabilitation of Ihiala Township Stadium, in Ihiala LGA, Anambra State

COST: N10 million

This project has been abandoned, and it is highly prone to mismanagement, as community members report it has been in existence for at least a decade. Testimonies from residents suggest this project has been repeatedly provided for in budgets annually, despite an apparent lack of willingness to deliver.

MINISTRY	AGENCY	ITEMS	AMOUNT	STATUS	OBSERVATION
LABOUR	NDE	TRAINING AND REINSATEMENT OF MEMBERS OF ORUMBA FARMERS COOPERATIVE SOCIETY IN ORUMBA NORTH/SOUTH FEDERAL CONSTITUENCY, ANAMBRA STATE	20,000,000	NOT DONE	COMMUNITY MEMBERS WERE NOT AWARE OF THIS PROJECT, THOUGH A GREAT MAJORITY ARE FARMERS
LABOUR	NDE	COMPLETION OF COMMUNITY LIBRARY PROJECT AT AWGBU, ORUMBA NORTH, ANAMBRA STATE	10,000,000	ONGOING	PROJECT HAS BEEN ABANDONED; LIBRARY CONSTRUCTION STOPPED AT FOUNDATION LEVEL.
WATER	AIRBA	COMPLETION OF COMMUNITY WATER PROJECT AT ST. JOSEPH'S CATHOLIC CHURCH, UMUNZE, ORUMBA SOUTH LGA, ANAMBRA STATE	10,000,000	ONGOING	PROJECT WAS INITIALLY ABANDONED BUT AFTER ENGAGEMENT WITH THE COMMUNITY AND THE REP. RESPONSIBLE FOR THE SITE, WORK HAS STARTED.
SCIENCE	ECN	PROVISION OF SOLAR POWERED STREET LIGHT IN SUNDRY COMMUNITIES OF ORUMBA NORTH/SOUTH FEDERAL CONSTITUENCY, ANAMBRA STATE	10,000,000	COMPLETED	PROJECT IMPLEMENTED.
LABOUR	NDE	COMPLETION OF A BLOCK OF 3 CLASSROOM WITH OFFICE AND VIP TOILET AT CENTRAL SCHOOL AMESI, AGUATA FEDERAL CONSTITUENCY OF ANAMBRA STATE	6,000,000	COMPLETED	STUDENTS NOW HAVE A CONDUCTIVE AND GOOD ENVIRONMENT FOR LEARNING.
LABOUR	NDE	SUPPLY AND INSTALLATION OF 500 KVA TRANSFORMER AT ISUOFIA, AGUATA FEDERAL CONSTITUENCY, ANAMBRA STATE	6,000,000	COMPLETED	THE COMMUNITY NOW HAS POWER SUPPLY WHICH HAS LED TO AN INCREASE IN ECONOMIC ACTIVITIES IN ISUOFIA.
LABOUR	NDE	PROVISION OF 15 POLES OF SOLAR STREET LIGHT AND SERVICING OF OLD SOLAR STREET LIGHT IN AGUATA FEDERAL CONSTITUENCY OF ANAMBRA STATE	15,000,000	COMPLETED	PROJECT IMPLEMENTED.
LABOUR	NDE	FENCING OF COMMUNITY CIVIC CENTRE IN UMUONA, AGUATA FEDERAL CONSTITUENCY, ANAMBRA STATE	8,000,000	ONGOING	WORK STILL ONGOING ON PROJECT SITE
WOMEN AFFAIRS	WOMEN AFFAIRS	SUPPLY AND INSTALLATION OF 500 KVA TRANSFORMER AT OKIJA WARD 4, IHIALA LGA, ANAMBRA STATE	6,000,000	COMPLETED	THE COMMUNITY IN OKIJA WARD 4 REPORTS COMPLETION OF THIS PROJECT, ENABLING THEIR ACCESS TO POWER, EVEN THOUGH SUPPLY IS PERIODICALLY INTERRUPTED
WOMEN AFFAIRS	WOMEN AFFAIRS	SUPPLY AND INSTALLATION OF 500 KVA TRANSFORMER AT UMUDARA, IHIALA, IHIALA LGA, ANAMBRA STATE	6,000,000	ONGOING	TRANSFORMER SUPPLIED AS AT TIME OF VISIT BUT INSTALLATION IS STILL ONGOING
YOUTH	YOUTH	REHABILITATION OF IHIALA TOWNSHIP STADIUM, IN IHIALA LGA, ANAMBRA STATE	10,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
TRADE	SMEDAN	STRATEGIC EMPOWERMENT PROGRAMME IN IHIALA LGA, ANAMBRA STATE	28,000,000	NOT DONE	COMMUNITY MEMBERS STATE THAT THIS EMPOWERMENT PROGRAM DID NOT TAKE PLACE IN IHIALA.
EDUCATION	EDUCATION	CONSTRUCTION OF A BLOCK OF 3 CLASSROOMS WITH VIP TOILET, FURNITURE, BOOKS, WATER HANDPUMP IN OGBUNIKE, OYI LGA , ANAMBRA STATE	20,000,000	COMPLETED	THE SCHOOL WHERE THIS PROJECT WAS IMPLEMENTED IS NOW AMONG THE BEST IN OGBUNIKE, AND THE HAND-PUMP PROVIDES POTABLE WATER .
ENVIRONMENT	ENVIRONMENT	ODIDA ABATETE EROSION/FLOOD CONTROL, ANAMBRA STATE.	20,000,000	ONGOING	WORK IS STILL ONGOING
HEALTH	PRIMARY HEALTH CARE	COMPLETION OF HEALTH CENTRE PROJECTS IN TOWNS IN ANAMBRA CENTRAL SENATORIAL DISTRICT	35,000,000	ONGOING	WORK IS STILL ONGOING
LANDS	LAND AND HOUSING	COMPLETION, EQUIPPING AND FURNISHING OF CIVIC CENTRE ALOR, IDEMILI SOUTH, ANAMBRA CENTRAL SENATORIAL DISTRICT	30,000,000	ONGOING	COMMUNITY MEMBERS SAID THEY WOULD HAVE PREFERRED MARKET STALLS INSTEAD OF THE CIVIC CENTER
LANDS	LAND AND HOUSING	SOLAR STREET LIGHTS (DOUBLE PANEL) AT ALOR AND SOME OTHER TOWNS IN ANAMBRA CENTRAL SENATORIAL DISTRICT	30,000,000	COMPLETED	RESIDENTS REPORT THAT WITH ELECTRIFICATION OF ALOR TOWN, MOVEMENT AT NIGHT IS EASIER AND HIGH CRIME RATES ARE REDUCED

MINISTRY	AGENCY	ITEMS	AMOUNT	STATUS	OBSERVATION
LAND	LAND AND HOUSING	SOLAR PANEL WATER BOREHOLES WITH OVER HEAD TANKS IN FOUR TOWNS IN ANAMBRA CENTRAL SENATORIAL DISTRICT) AT ALOR AND SOME OTHER TOWNS IN ANAMBRA CENTRAL SENATORIAL DISTRICT	30,000,000	COMPLETED	WITH THE LIGHTNING OF ALOR TOWN, IT MAKES MOVEMENT AT NIGHT EASIER AND REDUCE HIGH RATE OF CRIME AT NIGHT.
LAND	LAND AND HOUSING	SOLAR PANEL WATER BOREHOLES WITH OVER HEAD TANKS IN FOUR TOWNS IN ANAMBRA CENTRAL SENATORIAL DISTRICT) AT ALOR AND SOME OTHER TOWNS IN ANAMBRA CENTRAL SENATORIAL DISTRICT	35,000,000	COMPLETED	THIS PROJECT HAS BROUGHT POTABLE WATER TO THE COMMUNITIES BUT WE NOTE THAT MOST OF THE SOLAR PANELS ARE NO LONGER WORKING
LAND	LAND AND HOUSING	SUPPLY OF BUS SHELTERS IN 10 TOWNS IN ANAMBRA CENTRAL SENATORIAL DISTRICT	20,000,000	COMPLETED	TRAFFIC CONGESTION NOW REDUCED IN MOST JUNCTIONS IN TERMS OF ILLEGAL DROP-OFF OF PASSENGERS. WE HOWEVER OBSERVED THAT THE BUS SHELTER IS VERY SMALL AND NOT PROMINENT ENOUGH FOR SOME INTER STATE DRIVERS TO USE
SCIENCE	SHEDA	CONSTRUCTION OF SOLAR POWERED AT NORMU VILLAGE ENUGWUAGIDI, ANAMBRA STATE.	10,000,000	COMPLETED	UP AND RUNNING
WATER	WATER	CONSTRUCTION OF A BLOCK OF 3 CLASSROOMS WITH VIP TOILET AT UMUCHU, AGUATA LGA, ANAMBRA STATE	14,000,000	NOT DONE	PROJECT NOT IMPLEMENTED; COMMUNITY REPORTS IT NEEDS CLASSROOM BLOCKS AND A HALL FOR THE COMMON ENTRANCE EXAM FOR PUPILS.
WATER	WATER	REHABILITATION OF CLASSROOM BLOCKS AT ORAERI, IKENGA, AKPO, AMESI AND ACHINA, AGUATA LGA, ANAMBRA STATE	22,500,000	COMPLETED	THERE ARE NO MORE LEAKING ROOFS IN THE CLASSROOM, MAKING A MORE CONDUCIVE FOR LEARNING.
WATER	WATER	REHABILITATION OF CLASSROOM BLOCKS AT OGBOJI, ENUGU UMUONYIBA, ONEH AND IHITE IN ORUMBA SOUTH LGA, ANAMBRA STATE	18,000,000	ONGOING	REHABILITATION IS STILL ONGOING
WATER	WATER	REHABILITATION OF CLASSROOM BLOCKS IN IHEMBOSI, EKWUSIGO LGA., ANAMBRA STATE	4,500,000	NOT DONE	PROJECT WAS NOT IMPLEMENTED; COMMUNITY MEMBERS STATE A MORE PRESSING NEED IS A GOOD ACCESS ROAD
WATER	WATER	REHABILITATION OF CLASSROOM BLOCKS IN EKWULUMMILI, UTUH, AND EZINIFITE NNEWI SOUTH LGA, ANAMBRA STATE	13,500,000	ONGOING	WORK IS STILL ONGOING
WATER	WATER	COMPLETION OF CLASSROOM BLOCK AT AKWAIHEDI IN NNEWI SOUTH LGA, ANAMBRA STATE	2,000,000	COMPLETED	PROJECT IMPLEMENTED.
WATER	WATER	PROVISION OF 500 KVA TRANSFORMER AT THE ANAMBRA STATE UNIVERSITY, ULI, IHIALA LGA, ANAMBRA STATE	5,000,000	ONGOING	SUPPLIED BUT NOT YET INSTALLED.
WATER	WATER	PROVISION OF 500 KVA TRANSFORMER AT THE ORSUMOGHU, IHIALA LGA, ANAMBRA STATE	5,000,000	ONGOING	SUPPLIED BUT NOT YET INSTALLED.
WATER	WATER RESOURCES	CONSTRUCTION OF COMMUNITY RESOURCE CENTRE WITH INFRASTRUCTURE AT UGA, AGUATA LGA, ANAMBRA-SOUTH SENATORIAL DISTRICT, ANAMBRA STATE	55,000,000	ONGOING	SUPPLIED BUT NOT YET INSTALLED.

OGUN STATE

NO. OF PROJECTS TRACKED	COMPLETED	ONGOING	NOT DONE
29	9	2	18

tracka
www.tracka.ng

SAMPLE PROJECTS

PROJECT: Empowerment and Training of Youths in Ifo/Ewekoro Federal Constituency, Ogun State

COST: N55 million

Of three major empowerment programs in the 2015 budget for Ogun State's constituencies, the empowerment and training of youths in Ifo and Ewekoro has not been conducted, and PTOs report that the people were unaware of the project in its entirety before BudgIT's intervention.

PROJECT: Entrepreneur Development at Agro-Processing Centre, Owode, Ogun State

COST: N40 million

The agro-processing center building in the community was non-functional as at the time of PTOs' visit and our engagement with residents revealed the project has always been redundant, and there was never any training scheme of any sort in the community.

The project remains abandoned, with bushes developing fast and taking over the site.

PROJECT: Construction Of Classroom Blocks (280m Sqr. Gfa) + Vip Toilet And Furniture In Odeda Lga, Ogun Central Senatorial District, Ogun State.

COST: N12 million

The location of this project was not specified therefore making it difficult to track its progress; this is a norm with constituency projects in Nigeria. There are several other projects with specifications and amount specified that fails to establish the project site. Provisions like this are extremely prone to misappropriation of funds and corruption.

PROJECT: Procurement and Installation of Cassava Processing Tools/Machineries at Idofa Cassava Processing Centre, Imeko Afon LGA, Ogun State West Senatorial District

COST: N15 million



Agro Processing Centre, Owode

Members of Idofa community are predominantly into farming; cassava is the primary produce, and is frequently sent to neighboring towns and States for commercial purposes.

Our interaction with the residents revealed the cassava-processing center was promised in 2013 and construction commenced in 2014. It remained uncompleted till 2015, with constituents stunned at what is literally a N15 million provision to equip an uncompleted building with processing tools and machinery.



Idofa Cassava Processing Centre

MINISTRY	AGENCY	PROJECT TITLES	AMOUNT	STATUS	OBSERVATION
NHRC	NHRC	EMPOWERMENT AND TRAINING OF YOUTHS IN IFO/EWEKORO FED. CONSTITUENCY	55,000,000	NOT DONE	NO TRAINING PROGRAMME WAS DONE FOR THE COMMUNITY YOUTHS
SCIENCE	FIIRO, OSHODI	ENTERPRENEUR DEVELOPMENT AT AGRO PROCESSING CENTRE, OWODE, OGUN STATE	40,000,000	NOT DONE	THE BUILDING EXISTS BUT NO ENTERPRENEUR TRAINING TOOK PLACE
SCIENCE	PEEMADE	PROVISION AND INSTALLATION OF TRANSFORMERS IN YEWA/IPOKIA	15,000,000	NOT DONE	NOTHING OF SUCH WAS SEEN
PRESIDENCY	NEMA	SUPPLY OF 85 UNITS OF MOTOR CYCLES @N126,000 TO ADO- ODO/OTA	10,710,000	NOT DONE	MOTORCYCLES WERE NOT SUPPLIED
PRESIDENCY	NEMA	SUPPLY OF A TRACTOR AND ACCESSORIES TO ADO- ODO/OTA	11,500,000	NOT DONE	NOT SUPPLIED
PRESIDENCY	NEMA	SUPPLY OF A 18 SEATER BUS TYPE B TO ADO-ODO/OTA	32,200,000	NOT DONE	NOT SUPPLIED
TRADE	SMEDAN	PROVISION OF TRICYCLE & MOTOR CYCLE MACHINES FOR YOUTH AND WOMEN EMPOWERMENT AT IKENNE,SAGAMU/REMO NORTH	55,000,000	DONE	SUPPLIED
WATER	OORBDA	CONSTRUCTION OF 33 Nos BOREHOLES AT ABEOKUTA	55,000,000	ONGOING	WORK IS ONGOING
SCIENCE	NIBRR	ULTRA MODERN KING PALACE WITH 200 SEATER HALL IJOUN- EGBADO NORTH	45,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
SCIENCE	NIBRR	2.SOUND PROOF 100 KVA GENERATOR FOR THE PALACE OF ONIJOUN OF IJOUN - EGBADO NORTH	10,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
NHRC	NHRC	EMPOWERMENT AND TRAINING OF YOUTHS IN ABEOKUTA NORTH,OBAFEMI-OWODE, ODEDA FEDERAL CONSTITUENCY	55,000,000	COMPLETED	PROGRAMME HAS TAKEN PLACE IN ABEOKUTA NORTH AND OBAFEMI OWODE, BUT NOT YET IN ODEDA
EDUCATION	UBEC	CONSTRUCTION OF A BLOCK OF 3 CLASSROOMS WITH VIP TOILETS IN LGA PRIMARY SCHOOL, MAKUN-IROKUN, OGUN WATERSIDE LGA, OGUN EAST SENATORIAL DISTRICT.	19,000,000	COMPLETED	CONSTRUCTION WORK HAS BEEN COMPLETED
EDUCATION	UBEC	CONSTRUCTION OF A BLOCK OF 3 CLASSROOMS WITH VIP TOILETS IN LGA PRIMARY SCHOOL, ISIRE, IJEBU EAST LGA, OGUN EAST SENATORIAL DISTRICT.	19,000,000	DONE	CONSTRUCTION WORK HAS BEEN COMPLETED
EDUCATION	UBEC	CONSTRUCTION OF A BLOCK OF 3 CLASSROOMS WITH VIP TOILETS IN ANSAR-UD-DEEN PRIMARY SCHOOL, IROLU- REMO IKENNE LGA, OGUN EAST SENATORIAL DISTRICT.	19,000,000	DONE	CONSTRUCTION WORK HAS BEEN COMPLETED
EDUCATION	UBEC	CONSTRUCTION OF A BLOCK OF 3 CLASSROOMS AT IDOMILA COMPREHENSIVE HIGH SCHOOL, IDOMILA, IJEBU NORTH EAST LGA, OGUN EAST SENATORIAL DISTRICT.	19,000,000	DONE	CONSTRUCTION WORK HAS BEEN COMPLETED
EDUCATION	UBEC	CONSTRUCTION OF A BLOCK OF 3 CLASSROOMS AT JAPARA HIGH SCHOOL, IJEBU-IGBO, OGUN EAST SENATORIAL DISTRICT.	17,000,000	DONE	CONSTRUCTION WORK HAS BEEN COMPLETED
EDUCATION	UBEC	CONSTRUCTION OF A BLOCK OF 3 CLASSROOMS WITH VIP TOILETS IN ANSAR-UD-DEEN HIGH SCHOOL, ISIWO IJEBU- ODE LGA, OGUN EAST SENATORIAL DISTRICT.	17,000,000	DONE	CONSTRUCTION WORK HAS BEEN COMPLETED

MINISTRY	AGENCY	PROJECT TITLES	AMOUNT	STATUS	OBSERVATION
EDUCATION	UBEC	CONSTRUCTION OF CLASSROOM BLOCKS (280M SQR. GFA) + VIP TOILET AND FURNITURE IN ODEDA LGA, OGUN CENTRAL SENATORIAL DISTRICT, OGUN STATE.	12,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
EDUCATION	UBEC	CONSTRUCTION OF CLASSROOM BLOCKS (280M SQR. GFA) + VIP TOILET AND FURNITURE IN EWOKORO LGA, OGUN CENTRAL SENATORIAL DISTRICT, OGUN STATE.	12,000,000	DONE	CONSTRUCTION HAS BEEN COMPLETED, WITH FURNITURE INSTALLED
EDUCATION	UBEC	CONSTRUCTION OF CLASSROOM BLOCKS (280M SQR. GFA) + VIP TOILET AND FURNITURE IN ABEOKUTA	12,000,000	ONGOING	WORK IS ONGOING BUT AT A SLOW PACE
LABOUR	NDE	COMPLETION OF 3 BLOCKS OF CLASSROOM (WITH VIP TOILET, FURNITURE AND BOREHOLE) AT LG PRIMARY SCHOOL, IGBESA, ADO ODO/OTTA LGA, OGUN WEST SENATORIAL DISTRICT, OGUN STATE.	10,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
LANDS	LANDS & HOUSING	CONSTRUCTION OF COMMUNITY CENTRE WITH FACILITIES IN ODEDA LGA, OGUN CENTRAL SENATORIAL DISTRICT, OGUN STATE.	12,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
LANDS	LANDS & HOUSING	CONSTRUCTION OF COMMUNITY CENTRE WITH FACILITIES IN EWOKORO LGA, OGUN CENTRAL SENATORIAL DISTRICT, OGUN STATE.	12,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
POWER	REA	SUPPLY AND INSTALLATION OF 500KVA TRANSFORMER AND CONNECTION TO NATIONAL GRID IN ODEDA LGA, OGUN CENTRAL SENATORIAL	7,500,000	NOT DONE	TRANSFORMER NOT SUPPLIED. THE COMMUNITY ARE NOT AWARE ABOUT THE PROJECT
POWER	REA	SUPPLY AND INSTALLATION OF 500KVA TRANSFORMER AND CONNECTION TO NATIONAL GRID IN EWOKORO LGA, OGUN CENTRAL SENATORIAL DISTRICT, OGUN STATE.	7,500,000	NOT DONE	TRANSFORMERS NOT SUPPLIED; COMMUNITY MEMBERS REPORT THEY ARE NOT AWARE OF THE PROJECT
SCIENCE	PROJECT DEV. INSTITUTE	PROCUREMENT AND INSTALLATION OF CASSAVA PROCESSING TOOLS/MACHINERIES AT THE IDOFA CASSAVA PROCESSING CENTRE, IMEKO AFON LGA, OGUN WEST SENATORIAL DISTRICT, OGUN STATE.	15,000,000	ABANDONED	PROJECT SITE HAS BEEN ABANDONED SINCE 2014
SCIENCE	NASENI	CONSTRUCTION OF SCIENCE LABORATORY FURNITURE, PROCUREMENT AND INSTALLATION OF SCIENCE LABORATORY EQUIPMENT AT OKE ODAN GRAMMAR SCHOOL, OKE ODA, YEWA SOUTH LGA, OGUN WEST SENATORIAL DISTRICT, OGUN STATE.	25,000,000	COMPLETED	PROJECT IMPLEMENTED
SCIENCE	ENERGY COMMISSION	ESTABLISHMENT OF SOLAR STREET LIGHTS IN OGUN WEST SENATORIAL DISTRICT, OGUN STATE.	30,000,000	NOT DONE	A TRANSFORMER WAS ONLY SEEN IN A COMMUNITY CALLED ILOBI WITHOUT ACCESSORIES AND IT IS YET TO BE CONNECTED
WOMEN		CONSTRUCTION OF TOWN HALL AT IFONYINTEDO, IPOKIA LGA, OGUN WEST SENATORIAL DISTRICT, OGUN STATE.	30,000,000	ONGOING	CONSTRUCTION STILL ONGOING AND IS NOTED AS AT LINTEL LEVEL AS AT TIME OF VISIT

GOMBE STATE

NO. OF PROJECTS TRACKED	COMPLETED	ONGOING	NOT DONE
33	14	0	19

tracka
www.tracka.ng

SAMPLE PROJECTS

PROJECT: Training Research and Development in Yamaltu/Deba Federal Constituency, Gombe State

COST: N75 million

This project is reported as unimplemented. Responses allude to sentiments that the vagueness of the scope of this project tilts it towards being prone to corruption.

PROJECT: Supply of Computers and other ICT Equipment at G.G.S.S, Tula Kaltungo LGA, Gombe State

COST: N20 million

PTOs classify this project as unimplemented, and report the school authorities recounting the numerous hurdles they encounter on a daily basis. Also, the school's hostel can no longer accommodate the rising number of students, and assistance is also needed in this regard, as well as provision to mitigate suffering brought on by inadequate water

supply. Of paramount concern to respondents was the lack of security fencing for the school's buildings, which jeopardises the safety of the students and teachers.

PROJECT: Advocacy and Sensitisation in Kaltungo/Shongon Federal Constituency, Gombe State


COST: N35 million

The project is noted by PTOs as not implemented, and the consensus on the ground from constituents is that N35 million is an outrageous sum for a project with no tangible, sustainable benefit called "advocacy and sensitisation."

MINISTRY	AGENCY	PROJECT TITLES	AMOUNT	STATUS	OBSERVATION
NHRC	NHRC	TRAINING RESEARCH AND DEVELOPMENT IN YAMALTU/DEBA FED. CONST. GOMBE STATE.	75,000,000	NOT DONE	THE PROJECT HAS NOT BEEN IMPLEMENTED.
EDUCATION	EDUCATION	SUPPLY OF LABORATORY EQUIPMENT AT G.D.S.S., FILIYA SHONGOM LGA, GOMBE STATE.	20,000,000	COMPLETED	THE SCHOOL LABORATORY IS IN A DIRE CONDITION AND REQUIRES SOME REHABILITATION
EDUCATION	EDUCATION	SUPPLY OF COMPUTERS AND OTHER ICT EQUIPMENTS AT G.G.S.S, TULA KALTUNGO LGA, GOMBE STATE.	20,000,000	NOT DONE	THE PROJECT HAS NOT BEEN IMPLEMENTED AND THE SCHOOL NEEDS ADDITIONAL HOSTELS TO ACCOMMODATE STUDENTS.
NHRC	NHRC	ADVOCACY AND SENSITIZATION IN KALTUNGO/SHONGOM FED. CONSTITUENCY, GOMBE STATE.	35,000,000	COMPLETED	THE PROJECT HAS BEEN COMPLETED.
WATER	UBRBDA	AGRICULTURAL SUPPORT PROGRAMME - SUPPLY OF FERTILIZER, SPRAYER AND AGRO CHEMICAL IN DUKKU/NAFADA FED. CONST., GOMBE STATE.	45,000,000	NOT DONE	RESIDENTS ARE UNAWARE OF THE PROJECT AND HAVE NOT RECEIVED THE PROVISIONS.
WOMEN	NCWD	NATIONAL CENTRE FOR WOMEN DEVELOPMENT (NCWD): SUPPLY OF TRICYCLES AND MOTORCYCLES TO DUKKU/NAFADA FED. CONST., GOMBE STATE.	30,000,000	NOT DONE	MOTORCYCLES WERE DISTRIBUTED IN DUKKU BUT NOT IN NAFADA
NHRC	NHRC	ADVOCACY AGAINST DISCRIMINATION OF HIV AT AKKO FED. CONST., GOMBE STATE.	30,000,000	DONE	THE PROJECT HAS BEEN COMPLETED.
NHRC	NHRC	SUPPORT FOR INTERNALY DISPLACED PERSONS IN AKKO FED. CONST. GOMBE STATE.	45,000,000	NOT DONE	
WATER	UBRBDA	AGRICULTURAL SUPPORT PROGRAMME: SUPPLY OF KNAPSACK SPRAYERS, AGRO CHEMICALS AND FERTILIZER TO BALANGA/BILLIRI FED. CONST., GOMBE STATE	35,000,000	COMPLETED	RESIDENTS CONFIRMED THEY RECEIVED SOME OF ITEMS.
JUSTICE	NAPTIP	PURCHASE OF EMPOWERMENT MATERIALS, SEWING MACHINES, GRANDING MACHINES, HAIR DRESSING EQUIPMENT AND FOOD ITEMS AT BALANGA/BILLIRI FED. CONST., GOMBE STATE.	40,000,000	COMPLETED	RESIDENTS CONFIRMED THEY RECEIVED SOME ITEMS HOWEVER CERTAIN ITEMS ON THE LIST ARE MISSING.
SGF	REFUGEES	SUPPLY OF MOTORCYCLES AND KEKE NAPEP AT GOMBE, KWAMI, FUNAKAYE LGA, GOMBE STATE.	75,000,000	NOT DONE	RESIDENT HAVE NOT RECEIVED THE PROVISIONS.
AGRIC		EROSION CONTROL OF POKWANGLI IN KALTUNGO LGA GOMBE SOUTH SENATORIAL DISTRICT	10,000,000	ONGOING	WORK IS ONGOING AT THE PROJECT SITE.
EDUCATION	EDUCATION	STREET LIGHTING WITHIN THE FEDERAL UNIVERSITY KASHERE IN GOMBE CENTRAL SENATORIAL DISTRICT	100,000,000	COMPLETED	THE PROJECT HAS BEEN COMPLETED.
SCIENCE	ENERGY COMMISSION	CONSTRUCTION OF SOLAR STREET LIGHT IN GOMBE CENTRAL	25,000,000	DONE	THE PROJECT HAS BEEN COMPLETED, THERE ARE VISIBLE STREETLIGHTS IN GOMBE STATE.
JUSTICE	HUMAN RIGHT COMMISSION	ADVOCACY AND SANITIZATION IN GOMBE SOUTH SENATORIAL DISTRICT	50,000,000	COMPLETED	THE PROJECT HAS BEEN COMPLETED IN THE FOUR DISTRICTS.
JUSTICE	HUMAN RIGHT COMMISSION	CHILDREN AND YOUTH EMPOWERMENT IN GOMBE SOUTH SENATORIAL DISTRICT	20,000,000	DONE	THE RESIDENTS WOULD LIKE SKILL ACQUISITION AND PRACTICAL EMPOWERMENT PROGRAMS.

MINISTRY	AGENCY	PROJECT TITLES	AMOUNT	STATUS	OBSERVATION
SCIENCE	ENERGY COMMISSION	CONSTRUCTION OF SOLAR STREET LIGHT IN SELECTED AREAS OF GOMBE NORTH SENATORIAL DISTRICT	27,000,000	COMPLETED	THE PROJECT HAS BEEN COMPLETED.
WATER	UBRBDA	COMPLETION OF 2014 WATER PROJECTS IN GOMBE NORTH SENATORIAL DISTRICT	24,000,000	COMPLETED	THE PROJECT HAS BEEN COMPLETED.
WATER	UBRBDA	COMPLETION OF WATER PROJECTS (RETENTION 2011-2013) GOMBE NORTH SENATORIAL DISTRICT	13,500,000	COMPLETED	THE PROJECT HAS BEEN COMPLETED.
WATER	UBRBDA	SUPPLY OF AGRIC INPUT IN GOMBE NORTH SENATORIAL DISTRICT	60,000,000	NOT DONE	THE PROJECT HAS NOT BEEN IMPLEMENTED.

Report Summary

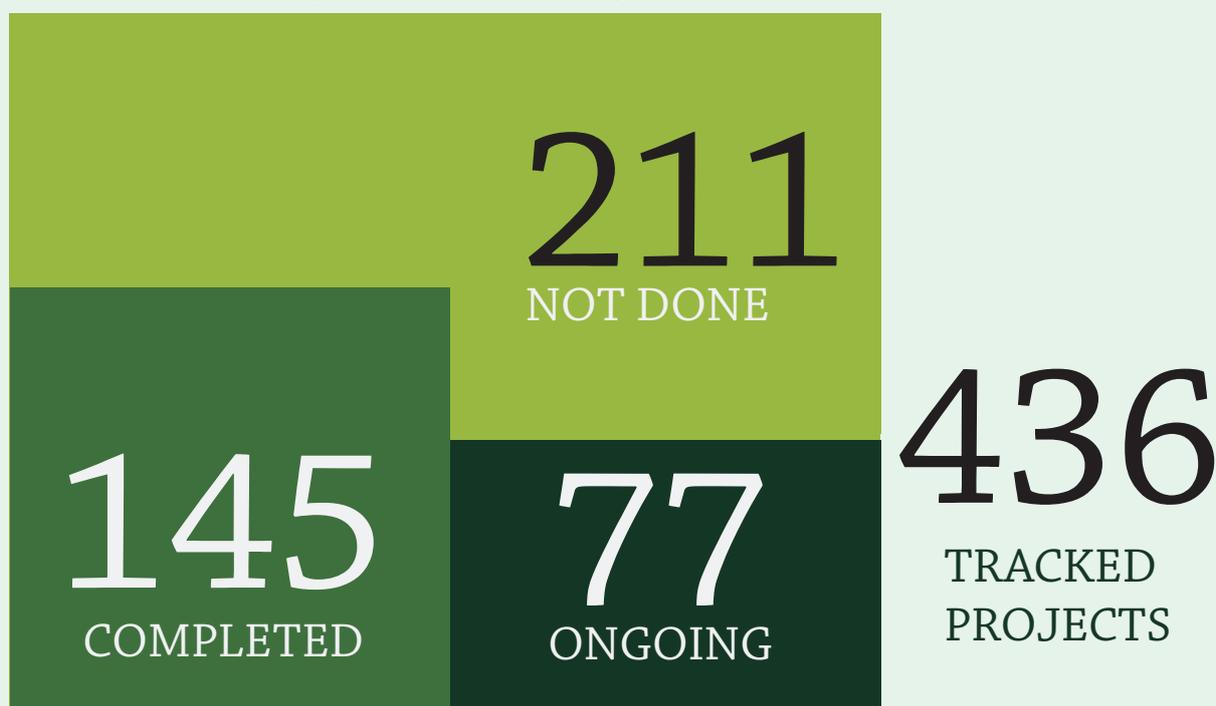

DELTA STATE

NO. OF PROJECTS TRACKED	COMPLETED	ONGOING	NOT DONE
30	12	9	9



SAMPLE PROJECTS

PROJECT: Comprehensive Health Centre at Etevie community, Delta State
COST: N15 million

We report this project as completed; community members expressed the belief that greater access to health care will drastically reduce mortality and improve the health of Etevie's indigenes.



Comprehensive Health Centre at Etevie Community

PROJECT: Rehabilitation of Block of 6 classrooms at Aka Primary School
COST: N10 million

PTOs report that this project has not been done. The primary school is one of two in the community, with the other school being an eyesore, as it is in much worse condition.



Ogwashi - Ukwu Dam

PROJECT: Renovation of Hostel at Ibru College Agbarha-Otor Ughelli
COST: N25 Million.

We gathered that the hostel repair work is completed; the building harbors students of the immediate academic community.



Ibru College, Agbarha, Otor Ughelli

PROJECT: Construction of Ogwashi-Ukwu Dam, Delta State
COST: N5.8 million

Work on this dam is ongoing, and workers were present at the project site at the time of visit. The Dam will ensure an adequate supply of water to the community, and irrigation of crops farmed by constituents of Ogwashi-Ukwu.

MINISTRY	AGENCY	ITEMS	AMOUNT	STATUS	OBSERVATION
SCIENCE	NAEC	GRADUATE TRAINING PROGRAMMES ORGANISED FOR DIFFERENT FEDERAL CONSTITUENCIES AT ISOKO FEDERAL CONSTITUENCY, DELTA STATE	165,000,000	NOT TRACKED	PROJECT UNACCESSIBLE FOR TRACKING
SGF	REFUGEES	PURCHASE OF PICK-UP VAN FOR ISOKO FEDERAL CONSTITUENCY, DELTA STATE	122,000,000	NOT TRACKED	PROJECT UNACCESSIBLE FOR TRACKING
NIGER DELTA	NIGER DELTA	MAINTENANCE OF SOLAR STREET LIGHTS IN ISOKO FEDERAL CONSTITUENCY, DELTA STATE	76,000,000	COMPLETED	SOLAR STREET LIGHTS SUPPLIED TO THE CONSTITUENCY AS AT THE TIME OF FIELDWORK
WORKS	WORKS	CONSTRUCTION OF ISOKO RING ROAD, DELTA STATE	142,000,000	NOT DONE	THIS ROAD DOES NOT EXIST, AND COMMUNITY MEMBERS REPORT THEY HAVE NO KNOWLEDGE OF THIS PROJECT
EDUCATION	UBEC	REHABILITATION OF BLOCK OF 6 CLASSROOMS AT ODION PRIMARY SCHOOL, EMEVOR, ISOKO FEDERAL CONSTITUENCY, DELTA STATE	10,000,000	COMPLETED	THE SCHOOL MANAGEMENT WERE SATISFIED WITH THE DRIVE OF WORK TO COMPLETION. MORE SCHOOLS NEEDED
EDUCATION	UBEC	REHABILITATION OF BLOCK OF 6 CLASSROOMS AT EVOJA PRIMARY SCHOOL, OLEH, ISOKO FEDERAL CONSTITUENCY, DELTA STATE	10,000,000	COMPLETED	THIS BUILDING CONSTRUCTION HAS BEEN IMPLEMENTED.
EDUCATION	UBEC	REHABILITATION OF BLOCK OF 6 CLASSROOMS AT OZADHE PRIMARY SCHOOL, ERAWHA, ISOKO FEDERAL CONSTITUENCY, DELTA STATE	10,000,000	ONGOING	WE OBSERVED THAT WORK IS IN PROGRESS; CONTRACTOR WAS SEEN AT PROJECT SITE.
EDUCATION	UBEC	REHABILITATION OF PRINCIPAL'S OFFICE AND STAFF ROOM AT OLOMORO COMPREHENSIVE HIGH SCHOOL, OLOMORO, ISOKO FEDERAL CONSTITUENCY, DELTA STATE	10,000,000	ONGOING	WE REPORT WORK AS ONGOING AS AT THE TIME OF VISIT TO THE PROJECT SITE
EDUCATION	UBEC	REHABILITATION OF PRINCIPAL'S QUARTER AT OTOR-OWHE GRAMMER SCHOOL, OTOR-OWHE, ISOKO FEDERAL CONSTITUENCY, DELTA STATE	10,000,000	ONGOING	WE OBSERVED THAT WORK IS IN PROGRESS; BUILDERS WAS SEEN AT ONSITE.
EDUCATION	UBEC	REHABILITATION OF PRINCIPAL'S OFFICE AT ATEBO COMPREHENSIVE HIGH SCHOOL, IYEDE, ISOKO FEDERAL CONSTITUENCY, DELTA STATE	10,000,000	COMPLETED	THIS HAS BEEN COMPLETED. THE TEACHERS WERE HAPPY WITH THE WORK.
EDUCATION	UBEC	REHABILITATION OF BLOCK OF 6 CLASSROOMS AT EGWARE PRIMARY SCHOOL, OZORO, ISOKO FEDERAL CONSTITUENCY, DELTA STATE	10,000,000	COMPLETED	PROJECT COMPLETED; STAFF REPORT SATISFACTION WITH QUALITY OF WORK DONE
EDUCATION	UBEC	REHABILITATION OF BLOCK OF 6 CLASSROOMS AT EMAMOKE PRIMARY SCHOOL, UZERE, ISOKO FEDERAL CONSTITUENCY, DELTA STATE	10,000,000	COMPLETED	THIS HAS BEEN IMPLEMENTED. THE KEY TO THE BUILDING HAS NOT BEEN HANDED OVER TO THE SCHOOL AUTHORITY.
EDUCATION	UBEC	REHABILITATION OF BLOCK OF 6 CLASSROOMS AT UZERE PRIMARY SCHOOL, UZERE, ISOKO FEDERAL CONSTITUENCY, DELTA STATE	10,000,000	COMPLETED	THIS HAS BEEN IMPLEMENTED; HOWEVER, KEYS TO THE BUILDING NOT YET GIVEN TO SCHOOL AUTHORITY.
EDUCATION	UBEC	REHABILITATION OF BLOCK OF 6 CLASSROOMS AT OWAWONA PRIMARY SCHOOL, ARAYA, ISOKO FEDERAL CONSTITUENCY, DELTA STATE	10,000,000	COMPLETED	THIS PROJECT HAS BEEN IMPLEMENTED
EDUCATION	UBEC	REHABILITATION OF BLOCK OF 6 CLASSROOMS AT EZETURO PRIMARY SCHOOL, EDHERIE, ISOKO FEDERAL CONSTITUENCY, DELTA STATE	10,000,000	COMPLETED	PROJECT IMPLEMENTED; COMMUNITY LEADERS REPORT THE SCHOOL NEEDS MORE CLASSROOMS
EDUCATION	UBEC	REHABILITATION OF BLOCK OF 6 CLASSROOMS AT OLORDO PRIMARY SCHOOL, OZORO, ISOKO FEDERAL CONSTITUENCY, DELTA STATE	10,000,000	ONGOING	WE OBSERVE WORK IS ONGOING, THE HEADMASTER REPORTS THE PACE IS OKAY; SAYS GOOD TOILETS NEEDED.
EDUCATION	UBEC	REHABILITATION OF BLOCK OF 6 CLASSROOMS AT AKA PRIMARY SCHOOL, UKPUDE, ISOKO FEDERAL CONSTITUENCY, DELTA STATE	10,000,000	NOT DONE	THIS HAS NOT BEEN IMPLEMENTED

MINISTRY	AGENCY	ITEMS	AMOUNT	STATUS	OBSERVATION
EDUCATION	UBEC	REHABILITATION OF BLOCK OF 6 CLASSROOMS AT ISI PRIMARY SCHOOL, ISI-EMEVOR, ISOKO FEDERAL CONSTITTUENCY, DELTA STATE	10,000,000	NOT DONE	NO REHABILITATION WORK HAS BEEN DONE IN THIS SCHOOL.
EDUCATION	UBEC	REHABILITATION OF BLOCK OF 6 CLASSROOMS AT ITIMI PRIMARY SCHOOL, IRRI, ISOKO FEDERAL CONSTITTUENCY, DELTA STATE	10,000,000	ONGOING	THE CONTRACTOR AND HIS MEN WERE SEEN WORKING; COMMUNITY MEMBERS REPORT THEY ALSO NEED POTABLE WATER
EDUCATION	UBEC	REHABILITATION OF BLOCK OF 6 CLASSROOMS AT IDHEZE PRIMARY SCHOOL, IDHEZE ISOKO FEDERAL CONSTITTUENCY, DELTA STATE	10,000,000	COMPLETED	PROJECT IMPLEMENTED
EDUCATION	UBEC	REHABILITATION OF BLOCK OF 6 CLASSROOMS AT IBAKPA PRIMARY SCHOOL, OFAGBE, ISOKO FEDERAL CONSTITTUENCY, DELTA STATE	10,000,000	COMPLETED	PROJECT IMPLEMENTED
EDUCATION	UBEC	REHABILITATION OF BLOCK OF 6 CLASSROOMS AT OKPOLO PRIMARY SCHOOL, OKPOLO-ENWHE, ISOKO FEDERAL CONSTITTUENCY, DELTA STATE	10,000,000	NOT TRACKED	NOT YET TRACKED
EDUCATION	UBEC	REHABILITATION OF BLOCK OF 6 CLASSROOMS AT ELLU PRIMARY SCHOOL, ELLU, ISOKO FEDERAL CONSTITTUENCY, DELTA STATE	10,000,000	COMPLETED	PROJECT IMPLEMENTED; HOWEVER SCHOOL TOILET NEEDS TO BE FIXED
EDUCATION	UBEC	REHABILITATION OF BLOCK OF 6 CLASSROOMS AT IKPIDIAMA PRIMARY SCHOOL, IKPIDIAMA, ISOKO FEDERAL CONSTITTUENCY, DELTA STATE	10,000,000	COMPLETED	THIS HAS BEEN IMPLEMENTED. THEY ENVISAGE FOR MORE SCHOOLS IN THEIR COMMUNITY
EDUCATION	UBEC	REHABILITATION OF BLOCK OF 6 CLASSROOMS AT EGBURIE PRIMARY SCHOOL, OZORO, ISOKO FEDERAL CONSTITTUENCY, DELTA STATE	10,000,000	COMPLETED	PROJECT IMPLEMENTED. RESIDENTS SEEK MORE SCHOOLS IN THEIR COMMUNITY
EDUCATION	UBEC	REHABILITATION OF BLOCK OF 6 CLASSROOMS AT EWERI PRIMARY SCHOOL, EMEDE, ISOKO FEDERAL CONSTITTUENCY, DELTA STATE	10,000,000	COMPLETED	PROJECT IMPLEMENTED; SCHOOL MANAGEMENT WANTS THE REMAINING BUILDINGS IN THE PREMISES REHABILITATED
EDUCATION	UBEC	REHABILITATION OF BLOCK OF 6 CLASSROOMS AT IGE PRIMARY SCHOOL, IGE, ISOKO FEDERAL CONSTITTUENCY, DELTA STATE	15,000,000	ONGOING	WE REPORT WORK AS ONGOING AS AT THE TIME OF VISIT TO THE PROJECT SITE.

EDO STATE

NO. OF PROJECTS TRACKED	COMPLETED	ONGOING	NOT DONE
18	5	2	11

tracka
www.tracka.ng

SAMPLE PROJECTS

PROJECT: Construction and furnishing of three classrooms, a headmaster's office, and a toilet at Akugbe primary school, Ukpogo in Uhunmwonde LGA, Edo South senatorial district

COST: N15 million

The project has been completed but is awaiting its official launch. The teachers and pupils of the school are delighted with the implementation of this project. Our PTOs' investigations gather that the old building was a death trap and a worsening wreck during rainy seasons.

PROJECT: Construction of Benin/Ademagbae-Egba-Akure Road (25km), Uhunmwode Local Government Area, Edo South senatorial district

COST: N400 million

We classify this project as ongoing, and the people of Egba community confirmed to PTOs that the construction of the road has increased economic activities in the area, easing farmers' and traders' access to the



Akugbe primary school, Ukpogo in Uhunmwonde

market. They also report that the contractor has absorbed quite a reasonable number of jobless youths in the community and thereby drastically reduced crime rates.



Benin/Ademagbae-Egba-Akure Road (25km)

PROJECT: Establishment of 38 number stand-alone solar power street light at Uhunmwode Local Government Area, Edo South Senatorial district
COST: N30 million

This project is noted as completed. The people of Urhokosa community were the beneficiaries of this stand-alone solar power street light project. Residents confirmed implementation was achieved in 2016, and the street light has helped reduce the excesses of hoodlums and increased security.

PROJECT: Horticulture Development in Irrua Specialist Hospital, Irrua Esan Central LGA, Edo State
COST: N25 million

Tracka's PTOs record this project as not implemented. Tracking officers subsequently engaged the secretary to the Zonal Medical Director, who states he is unaware of the existence of provision for this project in the budget.



Solar power street light at Uhunmwode

MINISTRY	AGENCY	ITEMS	AMOUNT	STATUS	OBSERVATION
WORKS	WORKS	"CONSTRUCTION OF BENIN/ADEMAGBAE-EGBA-AKURE ROAD,25KM, UHUNMWODE LOCAL GOVERNMENT AREA, EDO STATE"	400,000,000	ONGOING	PROJECT ONGOING AS AT TIME OF VISIT
EDUCATION	UBEC	CONSTRUCTION AND FURNISHING OF THREE CLASSROOMS, A HEADMASTER OFFICE AND TOILET AT UKPOGO, UHUNMWODE LGA, EDO STATE	15,000,000	COMPLETED	WE REPORT THIS PROJECT AS IMPLEMENTED
LANDS	LANDS	CONSTRUCTION OF URHOKUOSA TOWNSHIP ROAD (COMPLETION OF SIDE DRAINS AND ASPHALTING) UHUNMWODE LGA, EDO STATE	100,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
EDUCATION	UBEC	FURNISHING OF (6) CLASSROOMS AT IKEKEN PRIMARY SCHOOL, UROMI, ESAN NORTH EAST L.G.A EDO STATE	20,000,000	COMPLETED	THIS PROJECT HAS BEEN IMPLEMENTED AND READY FOR USE
EDUCATION	UBEC	CONSTRUCTION AND FURNISHING OF ONE BLOCK OF THREE (3) CLASSROOMS (OLD BLOCK)AT UKPEKO-IMIOKOLO PRIMARY SCHOOL, UROMI, ESAN NORTH EAST L.G.A EDO STATE.	5,000,000	ONGOING	PROJECT ONGOING AS AT TIME OF VISIT
EDUCATION	UBEC	RECLAMATION OF SADOH STREET, ANGLE 90, UROMI ESAN NORTH EAST LGA, EDO STATE. (SIDE DRAINS AND SAND FILLING)	5,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
ENVIRONMENT	ENVIRONMENT	SPECIALISED ENTREPRENUERIAL DEVELOPMENT SCHEME IN AKOKO EDO FEDERAL CONSTITUENCY, EDO STATE.	25,000,000	NOT DONE	NOT SUPPLIED
TRADE	SMEDAN	SUPPLY OF STARTER KITS FOR WELDING OF FABRICATIONS, BEAD MAKING, CARPENTRY AND FURNITURE MAKING, STYLING AND HAIRDRESSING, FASHION DESIGNING, BARBING, PHOTOGRAPHY, ILING, ELECTRICAL INSTALLATIONS ,PLUMBING AND PIPE FITTING TO AKOKO EDO FEDERAL CONSTITUENCY, EDO STATE.	20,500,000	NOT TRACKED	PROJECT NOT IMPLEMENTED
TRADE	BORBDA	PROVISION OF MEDICAL EQUIPMENTS AND A SOUND PROOF GENERATOR FOR THE HEALTH CENTRS IN OKHORE OPOJI, EBUDIN, IBHILOLOLU AND ATUAGBO ESAN CETRAL LGA, IDOA, OGWA ESAN WEST LGA,	35,000,000	NOT DONE	INDIGENES OF AKOKO EDO LGA DENIED KNOWLEDGE OF DISBURSEMENT OF THESE EQUIPMENT
HEALTH	NPHCDA	HORTI-CULTURE DEVELOPMENT IN IRRUA SPECIALIST HOSPITAL, IRRUA ESAN CENTRAL LGA, EDO STATE.	25,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
AGRIC	OIL PALM RESEARCH	ELECTRIFICATION OF EKO-AIMUFUA, ADESAGBON, OBADAN, EVBUOHUAN AND UVBE COMMUNITIES IN UHUNMWODE LOCAL GOVERNMENT AREA OF EDO STATE	55,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
WATER	BORDA	PROVISION OF 4 HAND PUMP BOREHOLES AT IGBIRA CAMPS IN OWAN WEST LGA, EDO STATE	4,300,000	COMPLETED	PROJECT IMPLEMENTED; COMMUNITY MEMBERS REPORT THEY ARE ENJOYING THE FACILITY.
WATER	BORDA	PROVISION OF 6 HAND PUMP BOREHOLES IN OWAN EAST AND WEST LGAs, EDO STATE	12,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
WATER	BORDA	PROVISION OF 2 NOS. MOTORISED BOREHOLES EQUIPPED WITH SOLAR PUMP AT AKE AND IKHUERAN-OTUO IN OWAN EAST LGA, EDO STATE.	20,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
WATER	BORDA	SUPPLY COMMUTAL BUSES TO PSYCHIATRIC HOSPITAL BENIN CITY, EDO SOUTH SENATORIAL DISTRICT, EDO STATE.	110,000,000	NOT SUPPLIED	BUSES HAS NOT BEEN PURCHASED
HEALTH	PSYCHIATRIC HOSPITAL BENIN CITY	PROVISION OF AMBULANCE FOR IRRUA SPECIALIST HOSPITAL, EDO CENTRAL SENATORIAL DISTRICT, EDO STATE.	20,000,000	NOT SUPPLIED	THE AMBULANCE HAS NOT BEEN PURCHASED
LANDS	LANDS & HOUSING	PROVISION OF BOREHOLE FOR IRRUA SPECIALIST HOSPITAL, EDO CENTRAL SENATORIAL DISTRICT, EDO STATE.	10,000,000	NOT DONE	PROJECT NOT IMPLEMENTED

JIGAWA STATE

NO. OF PROJECTS TRACKED	COMPLETED	ONGOING	NOT DONE
29	19	2	8



SAMPLE PROJECTS

PROJECT: Completion of Sankara township road in Jigawa North West Senatorial district in Ringim LGA
COST: N100 million

PROJECT: Drilling of 8 nos hand pumps boreholes at Madori and Kaugama Federal Constituency
COST: N5 Million

The road project has reached completion. However, considering the robust sum of N100 million, we report the grossly substandard quality of the road.

The Tracka team visited Madori and Kaugama LGAs to observe the execution of these water projects; five boreholes are completed and functioning at different locations, while the other three are still outstanding.

The PTO records particularly the poor landscaping, a lack of appropriate traffic markings, and blind curves on the road. The Sankara township road grants access to other communities and considering the frequency of commuters that ply it, the road may capitulate in no time.

Residents urge the government to implement more infrastructural developmental project in rural areas.



Sankara township road



Hand pumps boreholes at Madori

PROJECT: Construction/ Completion of Gwani Earth Dam in Gwaram LGA
COST: N38 million

We observed the project as ongoing as at the time of field visits. The Community Head, explained the challenges residents go through to access clean water, he stressed constituents' concern over the slow progress of the project and urged the government to ensure its completion.



Construction/ Completion of Gwani Earth Dam in Gwaram LGA

PROJECT: One block of 2 Classrooms at Iyo in Kirika-Sama LGA
COST:N5 million

This project has not been implemented. PTOs observed that renovation work is ongoing in four of the six classrooms within the school premises. Community members reported that due to the state of the school, learning is impossible for pupils in Iyo community, saying this is why pupils in Iyo fail external examinations. The PTO was also informed that the community has no knowledge of the provision of brand new classroom block of classrooms in the budget.



One block of 2 Classrooms at Iyo in Kirika-Sama LGA

MINISTRY	AGENCY	ITEMS	AMOUNT	STATUS	OBSERVATION
WATER	HJRBDA	DRILLING OF 2 NOS SOLAR POWERED BOREHOLE MOTORISED WITH PUBLIC STAND POST AT M/ MADORI AND KAUGAMA FED CONST JIGAWA STATE.	15,000,000	COMPLETED	THIS PROJECT HAS BEEN IMPLEMENTED
WATER	HJRBDA	DRILLING OF 8 NOS HANDPUMP BOREHOLES M/ MADORI AND KAUGAMA FED CONST JIGAWA STATE.	5,000,000	COMPLETED	FIVE OF THE EIGHT BOREHOLES HAVE BEEN DRILLED AND SUPPLIED TO THE RESPECTIVE COMMUNITIES
EDUCATION	UBEC	CONSTRUCTION OF 3NOS BLOCK OF TWO CLASSROOMS AT MALLAM MADORI KAUGAMA FED CONST JIGAWA STATE.	18,000,000	COMPLETED	WE OBSERVED THE CLASSROOM HAS BEEN CONSTRUCTED AS AT THE TIME OF OUR VISIT TO THE COMMUNITY
WATER	HJRBDA	UPGRADE/IMPROVEMENT OF HADEJA TOWNSHIP WATER SUPPLY,HADEJA JIGAWA STATE.	38,000,000	NOT DONE	INDIGENES OF THE COMMUNITY REPORT THAT THE PROJECT HAS NOT BEEN IMPLEMENTED
SGF	BCDA	SUPPLY OOF TRICYCLES TO RINGIM/TAURA FED CONST OF JIGAWA STATE.	20,000,000	COMPLETED	THESE HAVE BEEN SUPPLIED TO THE COMMUNITY, AS CONFIRMED BY INDIGENES
TRADE	SMEDAN	SUPPLY OOF MOTORCYCLES TO RINGIM/TAURA FED CONST OF JIGAWA STATE.	18,000,000	COMPLETED	COMMUNITY MEMBERS CONFIRM THESE HAVE BEEN SUPPLIED
WATER	HJRBDA	CONSTRUCTION OF TUBE WELLS AND SUPPLY OF 2 WATER PUMPS MACHINE BIRNIN KUDU/BUJI FED COST JIGAWA STATE	30,000,000	COMPLETED	PROJECT IMPLEMENTED
SGF	REFUGEE	SUPPLY OF GRINDING MACHINE (8NO) I40 MODEL (GRANDNUT) IN BIRNIN KUDU/BUJI FED CONST JIGAWA STATE	8,000,000	COMPLETED	PROJECT IMPLEMENTED
EDUCATION	UBEC	BLOCK OF 2 ROOM CLASSROOM BLOCKS IN MIGA/ JAHUN JIGAWA STATE	18,000,000	COMPLETED	PROJECT IMPLEMENTED
WATER	HJRBDA	HANDPUMP BOREHOLES IN MIGA/JAHUN JIGAWA STATE	10,000,000	COMPLETED	PROJECT IMPLEMENTED
SGF	REFUGEE	PROVISION OF FERTILIZERS IN MIGA/ JAHUN JIGAWA STATE	10,000,000	COMPLETED	COMMUNITY MEMBERS CONFIRM THAT THESE HAVE BEEN SUPPLIED
WATER	HJRBDA	IMPROVEMENT OF WATER SCHEME OF ABUNABO TOWN IN GURI L.G.A JIGAWA STATE.	6,000,000	COMPLETED	PROJECT IMPLEMENTED
POWER	REA	COMPLETION OF HT FROM BATURA - MUSARI ABUNABO IN GURI L.G.A JIGAWA STATE	20,000,000	NOT DONE	COMMUNITY MEMBERS CONFIRM THAT THIS PROJECT HAS NOT BEEN IMPLEMENTED
EDUCATION	UBEC	ONE BLOCK OF TWO CLASSROOM AT IYO IN KIRIKA-SAMA L.G.A JIGAWA STATE	5,000,000	ONGOING	WE OBSERVE WORK AS ONGOING AT THE PROJECT SITE
WATER	HJRBDA	SUPPLY AND FIT HT AND LT FOR MATARAR ALHAZAI AND ARAWA- BATURIYA IN KKM LGA JIGAWA STATE	7,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
INFORMATION	NTA	COMPLETION OF GWARAM NTA LINK-UP CENTRE JIGAWA STATE	20,000,000	ONGOING	WE REPORT WORK AS ONGOING AT THE PROJECT SITE

MINISTRY	AGENCY	ITEMS	AMOUNT	STATUS	OBSERVATION
HEALTH	NPHCDA	FENCING OF GALAMBI PHC JIGAWA STATE	20,000,000	COMPLETED	PROJECT IMPLEMENTED
WATER	HJRBDA	HAND PUMP POWERED BOREHOLS IN BABURA/GARKI FED CONST JIGAWA STATE	30,000,000	COMPLETED	PROJECT IMPLEMENTED
WATER	HJRBDA	SMALL SCALE IRRIGATION SCHEME IN BABURA/GARKI FED CONST JIGAWA STATE	8,000,000	NOT DONE	RESIDENTS CONFIRM PROJECT HAS NOT BEEN IMPLEMENTED
WATER	HJRBDA	PURCHASE OF FERTILIZERS OF NPK/UREA IN DUTSE/KIYAWA JIGAWA STATE	30,000,000	COMPLETED	THIS HAS BEEN SUPPLIED TO THE RESPECTIVE COMMUNITY CONFIRMED BY INDIGENES
WATER	HJRBDA	EMPOWERMENT PROGRAMME: PROCUREMENT OF MOTOR CYCLES (JINGCHEN PRODUCTS) IN DUTSE/KIYAWA JIGAWA STATE	8,000,000	COMPLETED	THIS HAS BEEN SUPPLIED TO THE RESPECTIVE COMMUNITY CONFIRMED BY INDIGENES
POWER	REA	RURAL ELECTRIFICATION PROJECT OF MAIMAZARI/DANTUWO/HANNINGIWA/DANKUMBO/MA'AZU OF SULETANKARKAR L.G.A JIGAWA STATE	38,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
INTERIOR	NIS	INDUSTRIAL DATA BANK UPGRADE	38,000,000	COMPLETED	PROJECT IMPLEMENTED
AGRIC	AGRIC	COMPLETION OF SANKARA TOWNSHIP ROAD IN JIGAWA NORTH WEST SENATORIAL DISTRICT	100,000,000	COMPLETED	WE OBSERVE THAT THE ROAD HAS BEEN CONSTRUCTED
WATER	HJRBDA	CONSTRUCTION /COMPLETION OF GWANI EARTH DAM IN JIGAWA STATE	38,000,000	ONGOING	WE OBSERVE WORK IS ONGOING AT THE PROJECT SITE
EDUCATION	EDUCATION	CONSTRUCTION OF 1 NO. OF ONE BLOCK OF TWO CLASSROOM IN JIGAWA SOUTH WEST SENATORIAL DISTRICT (MIGA LGA)	9,000,000	COMPLETED	PROJECT IMPLEMENTED
HEALTH	PHC	PAYMENT OF OUTSTANDING BALANCE FOR THE COMPLETED PRIMARY HEALTH CARE CENTRE AT JA'E IN KAUGAMA LGA OF JIGAWASOUTH WEST SENATORIAL DISTRICT	10,000,000	COMPLETED	PROJECT IMPLEMENTED
JUSTICE	NHRC	ECONOMIC AND HUMAN EMPOWERMENT IN JIGAWA SOUTH WEST SENATORIAL DISTRICT (MIGA, JAHUN, KIYAWA, DUTSE, BIRNIN KUDU, BUJI AND GWARAM LGA)	30,000,000	COMPLETED	PROJECT IMPLEMENTED; AS TESTIFIED TO BY A BENEFICIARY
SGF	NRC	YOUTH AND WOMEN EMPOWERMENT IN JIGAWA SOUTH WEST SENATORIAL DISTRICT (MIGA, JAHUN, KIYAWA, DUTSE, BIRNIN KUDU, BUJI AND GWARAM LGA UNDER THE NATIONAL REFUGEE COMMISSION)	30,000,000	COMPLETED	PROJECT IMPLEMENTED
WATER	HJRBDA	CONSTRUCTION OF 180 NOS. TUBE WELLS AND PUMPING MACHINE (GENERATORS) AND PROCUREMENT OF 120 NOS. OF MOTORCYCLES IN JIGAWA SOUTH WEST SENATORIAL DISTRICT (MIGA, JAHUN, KIYAWA, DUTSE, BIRNIN KUDU, BUJI AND GWARAM LGAS)	31,000,000	COMPLETED	PROJECT IMPLEMENTED
WATER	HJRBDA	CONSTRUCTION OF SMALL SCALE IRRIGATION SCHEME IN KIRIKASAMMA AND GURI LGAS OF JIGAWA NORTH-EAST SENATORIAL DISTRICT @ 15,000,000 EACH	20,000,000	NOT DONE	PROJECT IMPLEMENTED
WATER	HJRBDA	YOUTH EMPOWERMENT IN JIGAWA NORTH EAST SENATORIAL DISTRICT	50,000,000	COMPLETED	PROJECT IMPLEMENTED
WORKS	WORKS	CONSTRUCTION OF 12KM RURAL LATERITE ROAD FROM GIDAN MUTU DAYA-TURABU-M/ALHAZAI IN KIRIKASAMMA LGA OF JIGAWA NORTH EAST SENATORIAL DISTRICT	36,000,000	NOT DONE	THE ROAD HAS NOT BEEN CONSTRUCTED AS AT THE TIME OF OUR VISIT AS RESIDENT COULD NOT ASSIST WITH DETAILS

KADUNA STATE

NO. OF PROJECTS TRACKED	COMPLETED	ONGOING	NOT DONE
17	3	7	7

tracka
www.tracka.ng

SAMPLE PROJECTS

PROJECT: Youth Development Center at Tohu Sabon Gari Federal Constituency
COST: N90 million

The building structure of the development center has been completed; residents confirmed the physical building has been existing since 2014 but add that it remains nonfunctional, due to a lack of working facilities.

They note that the center will vehemently engage and educate Youths in Sabon Gari and the neighboring villages but take issue with what they describe as the sum of N90 million being allocated to develop an already existing building that is still not in working order.



Youth Development Center at Tohu Sabon Gari

PROJECT: Medical Awareness Campaign/ Medical Mission/Supplies of Equipment In Kudan Makarfi, Kaduna
COST: N60 million

Residents of Makarfi and Kudan towns confirm to PTOs that the medical awareness campaign was held on the same day at the two communities, with a primary focus on the importance of hygiene.

Participants affirmed receipt of mosquito nets and eye screening tests, but report that without an effective monitoring and evaluation body, projects with huge allocations for supplies are prone to mismanagement of public funds.

PROJECT: Supply of Keke Napep to Kaduna North Federal Constituency
COST: N26 million

We record this project as not implemented. Of the 14 equipment supply

projects in the 2015 federal budget for Kaduna State, 6 have been disbursed, while 8 supply and empowerment projects remain outstanding.

In cases where the equipment was supplied, there is no tangible information on the quantity and quality of the products distributed. Across the board, residents complained that the supply of equipment and empowerment programs were often prone to funds embezzlement and favouritism in distribution.

PROJECT: Construction Of Nos Blocks of Classrooms, Furnishing and Provision of Borehole at Dogarawa ward, Sabon Gari
COST: N26 million

Tracka's PTOs report this project as not executed, and observed the school was in deplorable condition; the classes lacked furniture and the roofs leaked on rainy days.

The Staff Office is dilapidated, and pupils have to bring in their own desks and chairs to the school. The School teachers report that the classrooms are inadequate for the number of pupils and that there is no durable water provision for the facility. Students are therefore required to fetch water to the school daily. We note that respondents were astonished at the enormous sum provided for this project, and they urged PTOs to request the government ensures full project implementation.



Construction of Nos Blocks of Classrooms, Furnishing and Provision of Borehole at Dogarawa ward, Sabon Gari

MINISTRY	AGENCY	ITEMS	AMOUNT	STATUS	OBSERVATION
WORKS	WORKS	CONSTRUCTION OF ROADS - RING ROAD (JUSHI WARD), WARRI STREET, LAGOS STREET, YORUBA STREET, BABBAN TITI, HAYIN OJO- ZAZZAU GINNERY, KWANTERESHA, DOGARAWA, HAYIN DANYARO, LAYIN MAKABARTA, ABU (NORTH GATE), KADUNA, KADUNA STATE	240,000,000	ONGOING	PROJECT ONGOING AS AT TIME OF VISIT, WITH ABOUT 25% LEFT UNTIL COMPLETION
YOUTH	YOUTH	YOUTH DEVELOPMENT CENTRE AT TOHU, SABON GARI FEDERAL CONSTITUENCY, KADUNA STATE	90,000,000	ONGOING	STRUCTURE COMPLETED SINCE 2014 BUT FACILITIES REQUIRED ARE YET TO BE SUPPLIED
TRADE	SMEDAN	STRATEGIC MSMES INTERVENTION AND EMPOWERMENT PROGRAMMES AT SABON GARI FEDERAL CONSTITUENCY, KADUNA STATE	280,000,000	DONE	THE LG OFFICIAL REPORTED PROJECT IMPLEMENTATION BUT RESIDENTS SAY SELECTED PEOPLE BENEFITTED FROM SCHEME
WATER	UNRBDA	PAYMENT OF OUTSTANDING LIABILITIES FROM 2012 PROJECTS AT SABON GARI FEDERAL CONSTITUENCY, KADUNA STATE	40,000,000	UNABLE TO TRACK	NO ACCESS TO INFORMATION
EDUCATION	NECO	SUPPLY OF EDUCATIONAL MATERIALS TO MAKARFI/ KUDUN FED. CONSTITUENCY	20,000,000	NOT DONE	FIELD VISITS TO THE LOCAL EDUCATION OFFICE REVEAL THESE MATERIALS HAVE NOT BEEN SUPPLIED
WOMEN	NCWD	SUPPLY OF COASTER BUSES, SUPPLY OF KEKE NAPEP KADUNA NORTH FED. CONST.	30,000,000	NOT DONE	THESE ITEMS HAVE NOT BEEN SUPPLIED; RESIDENTS STATE SUCH EMPOWERMENT AID DOES NOT EXIST
WOMEN	NCWD	SUPPLY OF KEKE NAPEP AT KUDAN/MAKARFI FEDERAL CONSTITUENCY	30,000,000	DONE	WE REPORT SOME TRICYCLES WERE SIGHTED BEING USED AS LOCAL AMBULANCES, WITH OTHERS TAKEN TO ZARIA FOR TRANSPORT BUSINESS
HEALTH	NPHCDA	SUPPLY OF AMBULANCE IN MAKARFI/KUDAN FED. CONST.	30,000,000	DONE	THE ONE GIVEN TO GENERAL HOSPITAL MAKARFI WAS USED TO CONVEY CORPSES OUT OF MAKARFI DURING VISIT
HEALTH	NPHCDA	MEDICAL AWAERENESS CAMPAIGN/MEDICAL MISSION/SUPPLIES OF EQUIPMENT IN KUDAN/ MAKARFI FED. CONST.	60,000,000	DONE	MOSQUITO NETS WERE DISTRIBUTED AND FREE MEDICAL CARE GIVEN TO PEOPLE WITH HEALTH ISSUES.
WATER	UNRBDA	CONSTRUCTION OF SOLAR POWER STREET LIGHT IN KADUNA STATE.	60,000,000	IN PROGRESS	PROJECT AT COMPLETION STAGE; WITH LIGHTS AMPLY DISTRIBUTED ROUND THE METROPOLIS
AGRIC	NAFRA	CONSTRUCTION OF 4NOS BLOCKS OF CLASSROOMS, FURNISHING AND PROVISION OF BOREHOLE @ DOGARAWA WARD SABONGARI LGA KADUNA STATE	26,000,000	NOT DONE	PROJECT NOT IMPLEMENTED; SCHOOL OVERPOPULATED AS AT TIME OF VISIT
SGF	BCDA	SUPPLY OF KEKE NAPEP TO KADUNA NORTH FED CONST KADUNA STATE	26,000,000	NOT DONE	THESE EMPOWERMENT ITEMS HAVE NOT BEEN DISTRIBUTED
SGF	BCDA	SUPPLY OF KEKE NAPEP TO ZARIA FED CONST KADUNA STATE	26,900,000	DONE	RESIDENTS TESTIFY THAT THE ITEMS HAVE BEEN SUPPLIED AND SHARED ACCORDINGLY
SCIENCE	ECN	SUPPLY OF EMPOWERMENT MATERIALS IN KAURA FED CONST KADUNA STATE	28,400,000	UNABLE TO TRACK	NO ACCESS TO INFORMATION
SPECIAL DUTIES	SPECIAL DUTIES	225 NOS MOTORCYCLE MACHINES @ N126,000 EACH TO BE SUPPLIED AT KURMIN-JIBRIN IN KAGARKO LGA KADUNA STATE	28,350,000	DONE	PROJECT IMPLEMENTED; HOWEVER, EXACT NUMBERS SUPPLIED COULD NOT BE ASCERTAINED
EDUCATION	EDUCATION	REHIBLITATION OF OF KAYARDA-DANALHAJI ROAD LERE LGA KADUNA STATE	26,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
POWER	ELECTRICITY MANAGEMENT SERVICES LIMITED	EMPOWERMENT AND CAPACITY BUILDING FOR TEACHERS IN JEMA'A/SANGA FED CONST KADUNA STATE	28,000,000	NOT DONE	PROJECT NOT IMPLEMENTED; TEACHERS UNAWARE OF PROGRAMMES

KEBBI STATE

NO. OF PROJECTS TRACKED	COMPLETED	ONGOING	NOT DONE
32	18	4	11

tracka
www.tracka.ng

SAMPLE PROJECTS

PROJECT: Construction of 1 block of 3 classrooms at Sheikh Abdullahi Fodio college Gwandu, Kebbi state

COST: N8 million

This project has been completed though it is worth mentioning that the building materials are of inferior quality. PTOs also note that the school teachers reported disappointment at the outcome of the classroom project and were distinctly outraged at its cost. The most perfunctory tour around the building fails to hide the poor flooring and electrification of the classes; also, only one fan was allocated to each classroom.



Construction of 1 block of 3 classrooms at Sheikh Abdullahi Fodio

PROJECT: Construction of 6 nos of 3 classrooms blocks with VIP toilets; supply of primary school; books, teaching aids and furniture in Augie, Argungu, Arewa, Dandi, Suru and Bagudo LGAS in Kebbi North senatorial district
COST: N85 million

Work was ongoing at the project site as at the time of PTOs' visits; three classroom blocks were being constructed, but it bears reporting that the VIP toilet is in fact a pit latrine.

We confirm that the furniture has been distributed, but the books and other teaching aids were omitted. The storekeeper at the UBEC office lamented over the low shortage of learning materials, confirming that the last book supply was delivered in 2014.



Construction of 6 nos of 3 classrooms blocks with VIP toilets

PROJECT: Supply of NPK Fertilizer to Sakaba LGA, Kebbi State
COST: N10 million

Tracka's PTOs record this project as not implemented. Though farming is the primary occupation of Sakaba's residents, the 2014-2015 farming season was largely unproductive for the farmers, and they report that this informed their shock at being made aware of this provision by PTOs.

Most constituents registered their regret over the state of their farms at a period when they should have been enjoying access to fertilizers, while a few stated they received fertilizers but were requested to pay N6,000 from next season's harvest.

PROJECT: Construction of 1 Block of 3 Classrooms, Kebbi State
COST: N8 million

Our PTOs were unable to track this provision as the project location was not specified in the budget.

Though a PTO visited the State Ministry of Education Board to inquire about the project, there was no disclosure of the project site and beneficiaries. This is a common thread with constituency projects in the 2015 budget; where project titles and amounts are stated as line items but without mention of the actual site of the project.

MINISTRY	AGENCY	ITEMS	AMOUNT	STATUS	OBSERVATION
WATER	SOKOTO RIMA RIVER DEVELOPMENT AUTHORITY	SUPPLY OF FARMING IMPLEMENTS TO FARMERS IN KEBBI SOUTH SENATORIAL DISTRICT, KEBBI STATE	30,000,000	NOT DONE	NO SUPPLY OF FARMING IMPLEMENTS IN KEBBI SOUTH SENATORIAL DISTRICT WAS REPORTED, AS AT TIME OF PROJECT TRACKING
WATER	SOKOTO RIMA RIVER DEVELOPMENT AUTHORITY	SMALL IRRIGATION SCHEME IN KEBBI SOUTH SENATORIAL DISTRICT	30,000,000	NOT DONE	INDIGENES REPORT NO IRRIGATION SCHEME TOOK PLACE; THIS PROJECT WAS NOT IMPLEMENTED
WATER	SRRBDA	PROVISION OF MINOR IRRIGATION SCHEME AT KEBBI CENTRAL SENATORIAL DISTRICT	85,000,000	NOT DONE	PROJECT NOT IMPLEMENTED; FARMERS TESTIFY THEY HAD NO KNOWLEDGE OF PROJECT
EDUCATION	UBEC	"CONSTRUCTION OF 6 NOS. OF (3) THREE CLASSROOMS BLOCKS WITH VIP TOILETS, SUPPLY OF PRIMARY SCHOOL BOOKS, TEACHING AIDS AND FURNITURE IN AUGI, ARGUNGU, AREWA, DANDI, SURU AND BAGUDO LGAS IN KEBBI NORTH SENATORIAL DISTRICT"	85,000,000	COMPLETED	THE PROJECT HAS BEEN FULLY IMPLEMENTED, WITH FURNITURE AND BOOKS ALL SUPPLIED
SCIENCE	ENERGY COMMISSION	"CONSTRUCTION OF SOLAR STREET LIGHTS IN ZURU AND YURI EMIRATES IN KEBBI SOUTH SENATORIAL DISTRICT"	25,000,000	COMPLETED	PROJECT IMPLEMENTED, WITH CONSTRUCTION TESTIFIED TO AS DONE IN SELECTED VILLAGES
WATER	SRRBDA	SUPPLY AND DISTRIBUTION OF FERTILIZER IN ZURU/FAKAI/SAKABA L.G.A OF KEBBI STATE	55,000,000	COMPLETED	AS AT THE TIME OF MONITORING, FAKAI LGA WAS SOLE RECIPIENT FERTILIZER; RESPONDENTS IN ZURU AND SAKABA LGA WERE UNAWARE OF THE IS PROJECT
WATER	UNRBDA	SUPPLY OF NPK FERTILIZER TO SAKABA LGA KEBBI STATE	10,000,000	NOT SUPPLY	PROJECT NOT IMPLEMENTED; RESIDENTS EXPRESSED SHOCK AS THEY WERE UNAWARE OF NPK SUPPLY PROVISIONS IN THE BUDGET
WATER	UNRBDA	SUPPLY OF BORE HOLE TO SAKAKBA LGA KEBBI STATE	10,000,000	DONE	PROJECT INSTALLED IN SAKABA VILLAGE; INDIGENES ALSO EXPRESSED SATISFACTION
WATER	SRRBDA	SUPPLY OF MOTORCYCLES IN NGASKI, MRBLGA OF KEBBI STATE	30,000,000	NOT SUPPLIED	PROJECT NOT IMPLEMENTED; RESIDENTS REPORT NO DISTRIBUTION OF MOTORCYCLES IN NGASKI TOWN, COMPLAIN ABOUT NEGLECT
WATER	SRRBDA	SUPPLY OF WATER PUMPS IN NGASKI, MRB LGA OF KEBBI STATE	25,000,000	DONE	THIS PROJECT HAS BEEN IMPLEMENTED WITHIN THE TOWN OF NGASKI.
WATER	SRRBDA	CONSTRUCTION OF ONE BLOCK OF THREE CLASSROOMS AT SHEIKH ABDULLAHI FODIO COLLEGE GWANDU, KEBBI STATE	8,000,000	ONGOING	WE REPORT WORK AS ONGOING AS AT TIME OF VISIT BUT RESIDENTS SAY THE FUNDS ALLOCATED ARE NOT REFLECTED ON THE PROJECT
WATER	SRRBDA	CONSTRUCTION OF ONE BLOCK OF THREE CLASSROOMS AT ,KEBBI STATE	8,000,000	NOT DONE	THIS PROJECT WAS NOT IMPLEMENTED
SGF	REFUGEES	PROVISION OF SOLAR STREET LIGHTS IN GWANDU/ALIERO/JEGA FED CONST. KEBBI STATE	39,000,000	DONE	SOLAR STREET LIGHTS COMPLETED IN JEGA AND ALIERO, WITH PROJECT IN GWANDU ONGOING AS AT TIME OF TRACKING
SGF	REFUGEES	PURCHASE OF ASSORTED GRAINS IN KAMBA DANDI L.G.A KEBBI STATE	10,000,000	DONE	RESPONDENTS TESTIFY THAT GRAINS SUPPLIED TO KAMBA WERE CONVERTED TO LOANS
SGF	REFUGEES	PURCHASE OF ASSORTED GRAINS IN BUMA DANDI L.G.A KEBBI STATE	19,000,000	DONE	THE GRAINS SUPPLY TO BUMA DANDI WAS CONVERTED TO THEM AS LOAN
EDUCATION	UBEC	CONSTRUCTION OF TWO CLASSROOMS AT UNGUWAR KANTA- TUKURWA-KAMBA KEBBI STATE	6,500,000	COMPLETED	PROJECT IMPLEMENTED BUT RESIDENTS STATE THAT SUBSTANDARD MATERIALS WERE USED
EDUCATION	UBEC	CONSTRUCTION OF TWO CLASSROOMS AT ISLAMIYA OPPOSITE IBRAHIM BAWA HOUSE KEBBI STATE	6,500,000	LOCATION UNKNOWN	NO SPECIFIC LOCATION FOR PROJECT SITE

MINISTRY	AGENCY	ITEMS	AMOUNT	STATUS	OBSERVATION
EDUCATION	UBEC	CONSTRUCTION OF TWO CLSASSROOMS AT MASUDU ISLAMIYA NEAR MUDI PRI SCH KAMBA KEBBI STATE	6,500,000	COMPLETED	PROJECT FULLY IMPLEMENTED
EDUCATION	UBEC	SUPLY OF GRINDING MACHINES TO DISPLACE COMMUNITIES IN BAGUDO AND SURU L.G.A KEBBI STATE	6,500,000	COMPLETED	PROJECT FULLY IMPLEMENTED
SGF	BCDA	BORDER SECURITY IN PARTNERSHIP WITH LOCAL COMM. ASSISTED PROGRAMME I.E SUPPLY OF EQUIPMENTS SUCH AS MOTOR CYCLES, TOUCH LIGHT, RAIN BOOTS, RAIN COAT ETC FOR BORDER PATROL IN MAJE, BAGUDO LGA KEBBI STATE	20,000,000	NOT DONE	THIS ITEMS WERE NOT SUPLIED IN BOTH COMMUNITIES AS AT THE TIME OF VISIT.
NAVY	NAVY	SPECIAL SECURITY TRAINING FOR ANTI TERRORISM (UNIFORM AND ACCOUTREMENTS)	55,000,000	NO ACCCES	NO ACCESS TO THE PROJECT SITE
LAND	LAND	PLANNING SCHEME FOR URBAN RENEWAL IN BIRNIN KEBBI/KALGO FED CONST KEBBI STATE	25,000,000	NOT DONE	THERE IS NO PLANNING SCHEME FOUND IN BOTH COMMUNITIES.
SCIENCE	TECHNOLOGY INCUBATION CENTRE	SUPPLY OF SKILL ACQUISITION FACILITIES IN BIRNIN KEBBI, KEBBI STATE	15,000,000	DONE	THE PROGRAMME WAS IMPLEMENTED; MOST COMMUNITY MEMBERS EXPRESSED APPROVAL
WATER	SRRBDA	SOLAR BOREHOLES IN BIRNIN KEBBI,KEBBI STATE	15,000,000	NOT DONE	NO SPECIFIC LOCATION FOR THE PROJECT
SGF	REFUGEE	YOUTH AND WOMEN EMPOWERMENT (SUPPLY OF TRICYCLES,GRINDING MACHINES,SEWING MACHINES AND JINCHENG MOTOR CIRCLES FOR ARGUNGU,AUGIE FED CONST,KEBBI STATE	55,000,000	DONE	THE PROJECT WAS IMPLEMENTED IN AUGIE, BUT NOTED AS NOT DONE IN ARGUNGU

KOGI STATE


NO. OF PROJECTS TRACKED	COMPLETED	ONGOING	NOT DONE
31	8	3	20

tracka
www.tracka.ng

SAMPLE PROJECTS

PROJECT: Construction of 3kms Access Road with Drainages and Culvert at Eika Adagu New Layout, from Eika Adagu New Layout Junction, Before Smart Filling
COST: N80 million

We record this project as ongoing, and noted the progress of the 3km access road construction with the requisite drainages and culvert. The contractor engaged youths of the Eika community, and the PTO will return to monitor its completion, as the project will ease commuters' access to the town's primary local market.

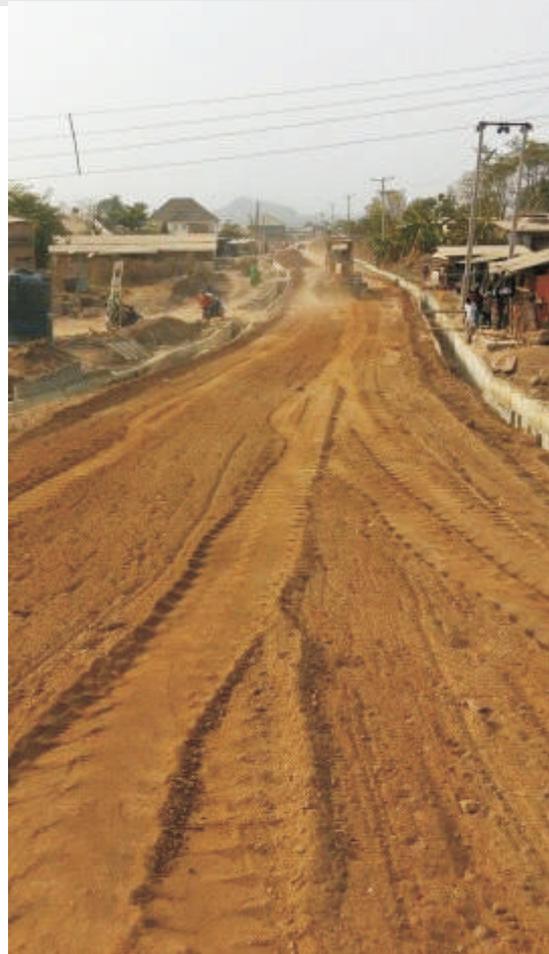

Construction of 3kms Access Road with Drainages and Culvert

PROJECT: Establishment of Cassava Processing Facility at Nagazi
COST: N50 million

This project has not been executed, despite its undeniable importance; the Nagazi community is the highest producer of cassava in Kogi state. Our engagement with constituents revealed the male residents are mostly into farming, with the women primarily involved in cassava flour production.

The Nagazi people stated they had no knowledge of the provision, during the town hall meeting where PTOs sensitized them on this line item and encouraged focused engagement with their representatives at the National Assembly to ensure delivery of this project.

PROJECT: Vocational training for 250 youth across Adavi/Okehi federal constituency, Kogi State
COST: N25 million

Residents of Adavi/Okehi LGA reported to PTOs as at the time of visit that they had not received the training neither were they aware of the project in the first place.

Our engagement with the people saw some youths expressing that this provision is prone to fraud and in cases where implemented, only members of the Senators' inner circles enjoy the resources.

PROJECT: Rehabilitation of broken-down borehole in some locations in Okene LGA, Kogi State
COST: N20 million

When the Tracka team met with members of the Okene community to discuss the status of boreholes in the area and visit project sites, it was revealed that this project has not been implemented.

Findings show some boreholes were installed in 2013 but are no longer functional. Therefore, residents still lack access to water and are subjected to walking long distances to fetch potable water.



Rehabilitation of broken-down borehole in some locations in Okene LGA, Kogi State

MINISTRY	AGENCY	ITEMS	AMOUNT	STATUS	OBSERVATION
TRADE	SMEDAN	100 UNITS OF TRICYCLES AT N48,800,000 = FOR YOUTH EMPOWERMENT AT DEKINA/ BASSA LGAs OF KOGI STATE	44,800,000	NOT DONE	PROJECT HAS NOT BEEN IMPLEMENTED
TRADE	SMEDAN	46 UNITS OF MOTORCYCLE AT N112,000 FOR YOUTH EMPOWERMENT AT DEKINA/BASSA LGAS OF KOGI STATE	5,200,000	NOT DONE	PROJECT HAS NOT BEEN IMPLEMENTED
SGF	REFUGEES	PROVISION OF GRAINS, RICE, SHELTERS, CLOTHING AND TOILETRIES FOR DISPLACED VICTIMS OF FULANI CRISES IN BAGANA, OMALA LGA. KOGI STATE	30,000,000	NOT DONE	WE OBSERVED WORK IS ONGOING AT THE PROJECT SITE.
JUSTICE	NAPTIP	PURCHASE OF GRINDING MACHINE MACHINES, HAIR SALOON EQUIPMENT MOTORCYCLES FOR EMPOWERMENT IN OLAMABORO IN OLAMABORO LGA KOGI STATE	20,000,000	UNABLE TO LOCATE	PROJECT HAS NOT BEEN IMPLEMENTED
WATER	LNRBDA	COMPLETION OF PROVISION OF SOLAR STREET LIGHTS IN COMMUNITIES IN YAGBA FEDERAL CONSTITUENCY	35,000,000	UNABLE TO LOCATE	UNABLE TO LOCATE
WORKS	FERMA	REHABILITATION OF EGBE OSI FEDERAL ROAD IN KOGI/KWARA STATES	15,000,000	NOT DONE	UNABLE TO LOCATE
JUSTICE	NAPTIP	VOCATIONAL TRAINING OF 300 WOMEN IN IDAH FEDERAL CONSTITUENCY, KOGI STATE	20,000,000	NOT DONE	PROJECT HAS NOT BEEN IMPLEMENTED
INFORMATION	NIGERIA FILM CORP.	SUPPLY OF EMPOWERMENT MATERIALS FOR 300 TRAINED WOMEN	30,000,000	UNABLE TO LOCATE	PROJECT HAS NOT BEEN IMPLEMENTED
INFORMATION	NIGERIA FILM CORP.	ENTERPRENEURSHIP TRAINING FOR 180 YOUTHS IN CINEMATOGRAPHY, STILL PHOTOGRAPHY, LINEAR EDITING AND SCRIPT WRITING	20,000,000	UNABLE TO LOCATE	ALL EFFORTS TO LOCATE THE PROJECT WERE UNSUCCESSFUL.
TRADE	SMEDAN	PROCUREMENT OF EQUIPMENT FOR THE TRAINEES IN NIGERIA FILM CORPORATION	30,000,000	UNABLE TO LOCATE	ALL EFFORTS BY THE TEAM TO LOCATE THE PROJECT WERE UNSUCCESSFUL.
TRADE	NAPTIP	PROVISION OF 250 UNITS MOTORCYCLES	32,500,000	UNABLE TO LOCATE	ALL EFFORTS BY THE TEAM TO LOCATE THE PROJECT WERE UNSUCCESSFUL.
MINES	RAW MAT EXPLORATORY AGENCY SMEDAN	PROVISION OF 30 UNITS TRYCLE	17,500,000	UNABLE TO LOCATE	ALL EFFORTS BY THE TEAM TO LOCATE THE PROJECT WERE UNSUCCESSFUL.
TRADE	SMEDAN	INVESTIGATION OF MINERAL RESOURCES OF AJAOKUTA LGA : RECONNAISSANCE SUVEY, MAPPING, DETAILED MINERAL INVENTORY, EXPLORATORY PITTING AND TRENCHING, TOPOGRAPHIC SURVEY, CHEMICAL ANALYSIS OF 200 SAMPLES, RESERVE DETERMINATION OF SELECTED MINERALS AND REPORT SUBMISSION.	50,000,000	NOT DONE	UNABLE TO LOCATE
MINES	NSRMEA	SPECIALISED ENTREPRENURSHIP PROGRAMME FOR YOUTHS IN OKENE LGA, KOGI STATE	20,000,000	NOT DONE	PROJECT HAS NOT BEEN IMPLEMENTED
JUSTICE	NAPTIP	TRAINING ON LOCAL MINING & QUARRYING METHODS FOR LOCAL MINERS IN OGORI MANGOGO LGA. KOGI STATE	30,000,000	NOT DONE	PROJECT HAS NOT BEEN IMPLEMENTED
JUSTICE	NAPTIP	PROVISION OF EMPOWERMENT MATERIAL FOR 250 YOUTHS ACROSS ADAVI/OKEHI FEDERAL CONSTITUENCY KOGI STATE	25,000,000	NOT DONE	NONE OF THE CONSTITUENTS WERE AWARE OF THIS PROGRAMME, NEITHER COULD THEY ATTEST TO ITS IMPLEMENTATION

CROSS RIVER STATE

NO. OF PROJECTS TRACKED	COMPLETED	ONGOING	NOT DONE
24	5	7	12

tracka
www.tracka.ng

SAMPLE PROJECTS

PROJECT: Completion of New Jerusalem Bridge Road, Agbokim Water Falls Cross River COST: N50 million

The New Jerusalem Bridge road is assumed to be a linkage between Cross River state and Cameroon; to promote fluid trade and services between Nigeria and Cameroon. In the 2015 Constituency project fund, N50mn was allocated for the realization of this project. Tracka's research on the project found that the bridge which was budgeted for is abandoned.

BudgIT Research also found that there were allocations for the same New Jerusalem Bridge road in constituency budgets for the years 2013 and 2014.

PTOs in Cross River State were able to ascertain that project work commenced on the proposed site in

2013 and after some time, the project was abandoned.



Completion of New Jerusalem Bridge Road, Agbokim

PROJECT: Procurement of Advanced Life Support Ambulance at University of Calabar Teaching Hospital Clinic Okoyong, Cross River State

COST: N62.5 million

This project, as provided for in the 2015 budget is reported as not implemented. As at the time of fieldwork, the ambulance, budgeted for N62.5m, has not been procured.

Although the focus of PTOs is primarily on the acquisition of the ambulance, our team extracted information about the lack of equipment in the clinic. Where equipment was present, it was in a less than stellar state. We surmise that two of the immediate needs of the clinic are the ambulance and standard generators.

A resident doctor reported that when patients are required to be transferred to other hospitals for further medical examination, public buses and cars are solicited due to the non-availability of a clinic ambulance.

PROJECT: Provision of Water Projects in Selected Communities of Obubra LGA

COST: N187 million

These water projects, termed “Zonal Intervention Projects” for some selected communities in Obubra LGA have been partially implemented. PTOs visited seven (7) beneficiary communities to assess implementation and notes that the project design is a solar-powered borehole equipped with two overhead plastic tanks for each of the communities. Unfortunately, Obubra LGA as a whole still lacks water supply,

due to its location and topography. Constituents report that it would be a great relief if all boreholes are made functional, as it would relieve them of the physical strain of walking kilometers before access to clean water.



Provision of Water Projects in Selected Communities of Obubra LGA

PROJECT: Provision of 50 Tricycles for Empowerment of 50 Youths in Calabar South/Bakassi/Akpabuyo Federal Constituency

COST: N32.5 million

The Tricycle Empowerment programme was expected to have been fully implemented in 2015, with the aim of employing youths and easing transportation in these communities.

Upon commencement of fieldwork, representatives of Bakassi and Akpabyo federal constituencies informed PTOs about the location of the tricycles and stated that the tricycles were being stored for later distribution.

Other observations as noted by PTOs as at the time of the tracking exercise is that the tricycles were yet to be fully acquired and those already purchased were stored in

the residence of a representative. The tricycles are covered in dust, due to long-term abandonment while some are reported as already developing mechanical faults and in poor condition due to non-use.



Provision of 50 Tricycles for Empowerment of 50 Youths in Calabar South/Bakassi/Akpabuyo Federal Constituency

MINISTRY	AGENCY	PROJECT TITLES	AMOUNT	STATUS	OBSERVATION
YOUTH	YOUTH	CONSTRUCTION/EQUIPPING OF NATIONAL YOUTH DEVELOPMENT CENTRE,AGBOKIUN WATER FALLS,CROSS RIVER (ON GOING)	100,000,000	ONGOING	THE PROJECT IS ONGOING.
LANDS	LANDS	COMPLETION OF NEW JERUSALEM BRIDGE/ROAD,AGBOKIM WATER FALLS CROSS RIVER	50,000,000	NOT DONE	THE PROJECT HAS NOT BEEN IMPLEMENTED
LANDS	LANDS	URBAN RENEWAL/DEVELOPMENT OF ESSENTIAL INFRASTRUCTURE IN AGBOKIM WATERFALLS, CROSS RIVERS (ON-GOING)	50,000,000	NOT DONE	THE PROJECT WAS LIFTED FROM THE 2014 BUDGET.
WATER	WATER	PROVISION OF WATER PROJECTS IN SELECTED COMMUNITIES OF OBUBRA LGA, CROSS RIVER	35,000,000	COMPLETED	COMPLETED, THERE ARE BOREHOLES ACROSS OBRUBA
HEALTH	UCTH	PROCUREMENT OF ADVANCE LIFE SUPPORT AMBULANCE FOR UNIVERSITY OF CALABAR TEACHING HOSPITAL CLINIC OKOYONG, CROSS RIVER STATE.	62,500,000	COMPLETED	PROJECT IMPLEMENTED; THE HOSPITAL HAS RECEIVED THE EQUIPMENT
LABOUR	NDE	PROVISION OF TRICYCLES FOR OBANLIKU/ OBUDU/ BEKWARRA LGA, CROSS RIVER STATE	22,500,000	NOT DONE	PROJECT NOT IMPLEMENTED AS AT THE TIME OF VISIT.
TRADE	SMEDAN	STRATEGIC EMPOWERMENT AND ENTERPRISE DEVELOPMENT INITIATIVE FOR WOMEN IN OBANLIKU/ OBUDU/ BEKWARRA LGA, CROSS RIVER STATE	20,000,000	NOT DONE	THE PROJECT HAS NOT BEEN IMPLEMENTED.
WATER	CRBDA	ENTERPRISE AND BUSINESS DEVELOPMENT FOR AGRICULTURE FARMS AND PARK MPCs ATAN-OKOYONG-ODUKPANI LGA, CROSS RIVER STATE.	32,500,000	COMPLETED	PROJECT IMPLEMENTED; YOUTHS REPORT THEY UNDERWENT TRAINING PROGRAMMES
TRADE	SMEDAN	BUILDING CAPACITY FOR THE AKIM ENTERPRISE INCUBATION CENTRE- CALABAR MUNICIPAL, ODUKPANI FEDERAL CONSTITUENCY, CROSS RIVER STATE	30,000,000	NOT DONE	THE PROJECT HAS NOT BEEN IMPLEMENTED.
WATER	CRBDA	COMPLETION OF IWURU ROAD AKAMKPA LGA, AKAMKPA/BIASE FDERAL CONSTITUENCY, CROSS RIVER STATE.	22,500,000	NOT DONE	PROJECT LOCATION UNKOWN AS THERE IS NO OTHER ROAD CONNECTING IWURU AND AKAMKPA, ASIDES THE FEDERAL HIGHWAY
WATER	CRBDA	REHABILITATION OF OBAN-EKAN ROAD AKAMKPA LGA, CROSS RIVER STATE.	40,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
LABOUR	NDE	PROVISION OF 50 TRICYCLES FOR EMPOWERMENT OF 50 YOUTHS (IN CALABAR SOUTH/ BAKASI/ AKPABUYO FEDERAL CONSTITUENCY ON CROSS RIVER STATE.	32,500,000	ONGOING	OUR ENGAGEMENT WITH THE RELATED OFFICIALS REVEALED TRICYCLES HAVE BEEN PROCURED AND WILL SOON BE DISTRIBUTED
LABOUR	NDE	SKILL AQUISITION TRAINING AND RESETTLEMENT OF 60 YOUTHS / WOMEN IN CALABAR SOUTH AND BAKASSI OF CROSS RIVER STATE	30,000,000	NOT DONE	THE PROJECT HAS NOT BEEN IMPLEMENTED.
EDUCATION	UBEC	SUPPLY OF SCIENCE EQUIPMENT AND LEARNING MATERIALS TO SELECTED SCHOOLS IN OGOJA/YALA FEDERAL CONSTITUENCY	20,000,000	COMPLETED	PROJECT IMPLEMENTED; SCIENCE EQUIPMENT AND LEARNING MATERIALS HAVE BEEN DELIVERED
EDUCATION	UBEC	SUPPLY OF LIBRARY BOOKS TO SELECTED SCHOOLS IN OGOJA/YALA FEDERAL CONSTITUENCY	20,000,000	DONE	COMPLETED, BOOKS HAVE BEEN DELIVERED TO THE SCHOOL
EDUCATION	UBEC	SUPPLY OF SCHOOL DESKS TO SELECTED SCHOOLS IN OGOJA/YALA FEDERAL CONSTITUENCY	22,500,000	COMPLETED	COMPLETED. DESKS HAVE BEEN SUPPLIED.
WATER	CRBDA	CONSTRUCTION OF EROSION CONTROL IN OBEKOKOWEN AND LOGAN NTAN EKORI OF ABI/YAKURR FEDERAL CONSTITUENCY OF CROSS RIVER STATE.	62,500,000	DONE	THE PROJECT HAS BEEN IMPLEMENTED

MINISTRY	AGENCY	PROJECT TITLES	AMOUNT	STATUS	OBSERVATION
DEFENCE	DEFENCE	RENOVATION WORKS AT ARMY BARRACKS, AFI IKOM	100,000,000	COMPLETED	THE PROJECT WAS COMPLETED IN 2014
EDUCATION	FMOE	FACULTY OF LAW BUILDING UNIVERSITY OF CALABAR	200,000,000	ONGOING	WE OBSERVED CONSTRUCTION WORKS AT THE PROJECT SITE
TRADE	SMEDAN	SUPPLY OF TRICYCLES TO SELECTED YOUTHS IN BOKI LGA CRS	50,000,000	NOT DONE	THE PROJECT HAS NOT BEEN IMPLEMENTED.
TRADE	SMEDAN	PROVISION OF WATER PROJECTS IN SELECTED COMMUNITIES OF OBUBRA LGA, CROSS RIVER	50,000,000	NOT DONE	THE PROJECT HAS NOT BEEN IMPLEMENTED.
TRADE	SMEDAN	SUPPLY OF GRINDING MACHINES TO SELECTED WOMEN IN OBUBRA LGA CRS	50,000,000	NOT DONE	THE PROJECT HAS NOT BEEN IMPLEMENTED.
TRADE	SMEDAN	SUPPLY OF GRINDING MACHINES TO SELECTED WOMEN IN YAKURR LGA CRS	50,000,000	NOT DONE	THE PROJECT HAS NOT BEEN IMPLEMENTED.
TRADE	SMEDAN	STRATEGIC EMPOWERMENT AND ENTERPRISE DEVELOPMENT INITIATIVE FOR WOMEN IN OBANLIKU/ OBUDU/ BEKWARRA LGA, CROSS RIVER STATE	20,000,000	NOT DONE	THE PROJECT HAS NOT BEEN IMPLEMENTED.
WATER	CRBDA	IRRUAN DAM	100,000,000	ONGOING	WE OBSERVED ONGOING WORKS AT THE DAM SITE
TRADE	SMEDAN	SUPPLY OF TRICYCLES TO SELECTED YOUTHS IN ABI LGA CRS	50,000,000	ONGOING	WE OBSERVED TRICYCLES HAVE BEEN PROCURED BUT ARE YET TO BE DISTRIBUTED
WATER	CRBDA	EROSION CONTROL WORKS AT AKPARABONG IKOM	100,000,000	COMPLETED	PROJECT IMPLEMENTED
WATER	CRBDA	FLOOD AND EROSION CONTROL WORK AT KAKWAGOM BOKI	50,000,000	NOT DONE	THE PROJECT HAS NOT BEEN IMPLEMENTED.
WATER	CRBDA	FLOOD/EROSION CONTROL BENKOKWA, ATAKAMBA AND KASHIE COMMUNITIES OF BANSAN OSOKOMWORKS AKAM	100,000,000	COMPLETED	PROJECT IMPLEMENTED
WATER	CRBDA	CONSTRUCTION OF WATER SHED THROUGH OGOJA ROAD TO ABEB RIVER IN OBUDU LGA, CROSS RIVER NORTH SENATORIAL DISTRICT, CROSS RIVER STATE.	110,000,000	ONGOING	WE OBSERVED ONGOING WORKS AT THE SITE
WATER	CRBDA	EROSION CONTROL IN ADIABO AKANIJOBIO-UKPAKATA, CROSS RIVER SOUTH SENATORIAL DISTRICT, CROSS RIVER STATE.	110,000,000	NOT DONE	THE PROJECT HAS NOT BEEN IMPLEMENTED.
YOUTH	FMYD	PROVISION OF BASIC INFRASTRUCTURE AT YOUTH DEVELOPMENT CENTRE IKOM	100,000,000	ONGOING	WORK IS ONGOING AT THE PROJECT SITE

IMO STATE

NO. OF PROJECTS TRACKED	COMPLETED	ONGOING	NOT DONE
29	8	9	12

tracka
www.tracka.ng

SAMPLE PROJECTS

PROJECT: Construction of Primary Healthcare Centre at Ikpeze, Ideato North Federal Constituency, Imo State

COST: N20 million

We confirm that construction of the primary health care center was completed in 2015. However, the facility lacks the necessary equipment to run optimally and provide efficient medical services to people in the community.

During fieldwork, majority residents expressed the opinion that the project is as good as incomplete without furnishings and equipment, as these are needed to serve patients better and help address medical issues in the area.



Primary Healthcare Centre at Ikpeze, Ideato

PROJECT: RENOVATION OF SIX (6) CLASSROOM BLOCK AT GROUP SCHOOL, MBUTU NWORIE, ABOH MBAISE, IMO STATE

COST: N30M

The renovation of six (6) classrooms at Group School, Mbutu Nworie of Imo state was implemented and equipped with new chairs and tables for each classroom. At the time of the tracking exercise, project

tracking officers noted that the presumed ix-classroom (6) block actually a five-classroom (5) block.

The information garnered during the tracking exercise from the correspondents is that the renovation of the classroom block has improved studying and made learning environment conducive different from when renovation was yet to commence.



Renovation Of Six (6) Classroom Block At Group School, Mbutu Nworie, Aboh Mbaise, Imo State

PROJECT: Completion of Rural Electrification at Obohia and Oru Autonomous Community, Ahiazu Mbaise
COST: N25 million

The scheme has so far shown installation of light poles, electric wires and transformers. From our research, the rural electrification project is pegged at a completion stage of 80%.

The PTOs' visit to the site of the rural electrification project for Obohia and Oru revealed that some activity is ongoing.



Rural Electrification at Obohia and Oru Autonomous Community, Ahiazu Mbaise

PROJECT: Construction of Solar-powered Borehole at Uwaoma Nnrambia, Ahiara, Ahiazu Mbaise

COST: N20 million

The solar-powered borehole construction project was completed in 2015. As at the time of PTOs' tracking visits, the borehole project was up and running, serving the community of Uwaoma Nnrambia Ahiara and Ahiazu Mbaise. Prior to the construction of the borehole, community members report they walked a long distance to get water from river banks and streams.



Solar-powered Borehole at Uwaoma Nnrambia, Ahiara, Ahiazu Mbaise

MINISTRY	AGENCY	PROJECT TITLES	AMOUNT	STATUS	OBSERVATION
NIGER DELTA	NIGER DELTA	CONSTRUCTION OF MBAISE RING ROAD, IMO STATE	400,000,000	ONGOING	PROJECT ONGOING BUT WORK WAS LAST NOTED IN EARLY 2015
NIGER DELTA	NIGER DELTA	CONSTRUCTION OF OKPALA-IGWURITA ROAD, IMO STATE	100,000,000	ONGOING	PROJECT ONGOING BUT WORK WAS LAST NOTED IN EARLY 2015
NIGER DELTA	NIGER DELTA	CONSTRUCTION OF CASSAVA PROCESSING FACILITY MBUTU, ABOH MBAISE, IMO STATE	20,000,000	ONGOING	PROJECT SITE IS FAR FROM COMMUNITY; RESIDENTS BARELY KNOW ABOUT ITS EXISTENCE.
POWER	TCN	132KVA/33 SUBSTATION AT IBEKU/AMAOHURU NGURU, IMO STATE	90,000,000	ONGOING	SCANTY WORK NOTICEABLE ON PROJECT; HOWEVER, SITE ENGINEER REPORTS WORK ONLY STOPPED DUE TO LOW FUNDS
POWER	TCN	PROCUREMENT AND INSTALLATION OF IX15MVA/33/11KVA TRANSFORMERS AND CONSTRUCTION OF INJECTION SUBSTATION AT ONICHA EZINIHITE, IMO STATE	60,000,000	ONGOING	PROJECT SITE IS COVERED WITH GRASS, SUGGESTING ABANDONMENT OF IMPLEMENTATION
YOUTH	YOUTH	FURNISHING OF YOUTH DEVELOPMENT CENTRE AT ABOH MBAISE, IMO STATE	20,000,000	ONGOING	BUILDING HAS BEEN COMPLETED BUT EQUIPMENTS FOR OPERATIONS ARE YET TO BE PUT IN PLACE
SCIENCE	NASENI	CONSTRUCTION OF AGRICULTURE MACHINERY DEVELOPMENT INSTITUTE, MBAISE	80,000,000	ONGOING	WORK IS IN PROGRESS
SCIENCE	NASENI	LIABILITY FOR THE NODAL EXPANSION FOR NASENI PROGRAMME AT AHIARA, AHIAZU MBAISE, IMO STATE	30,000,000	COMPLETED	ROAD HAS BEEN COMPLETED AND IS FULLY IN USE
ENVIRONMENT	ENVIRONMENT	PROCUREMENT AND INSTALLATION OF EQUIPMENT AT WASTE RECYCLING FACILITY AT OWERRI, IMO STATE	80,000,000	NOT DONE	PROJECT LOCATION IS UNKNOWN
WATER	AIRBDA	COMPLETION OF THE RECONSTRUCTION OF CHEMISTRY AND BIOLOGY LABORATORY AT ST. PATRICK'S SECONDARY SCHOOL, OGBE AHIARA, IMO STATE	8,000,000	COMPLETED	LABORATORY IS FULLY RENOVATED AND IN FULL OPERATION
WATER	AIRBDA	COMPLETION OF REHABILITATION OF FATHER WELSH ROAD EMEKUKU, OWERRI NORTH, IMO STATE	30,000,000	COMPLETED	ROAD IS TARRED, SUGGESTING REHABILITATION - BUT POTHOLES STILL EXIST
WATER	AIRBDA	COMPLETION OF CONSTRUCTION OF SOLAR POWERED BOREHOLE AT ST. PATRICK'S SECONDARY SCHOOL, OGBE AHIARA, IMO STATE	7,000,000	COMPLETED	THE BOREHOLE IS COMPLETED BUT IT WAS GATHERED THAT THE POWER BOX HAS BEEN STOLEN AFTER INCEPTION
AGRIC	NRCRI, IMUDIKE	COMPLETION OF CONSTRUCTION OF CASSAVA PROCESSING CENTRE AT OKWUABALA, ORLU, IMO STATE	20,000,000	COMPLETED	PROJECT IMPLEMENTED BUT CENTRE NOT YET IN USE; MAJORITY OF COMMUNITY MEMBERS ARE UNAWARE OF PROJECT. ALSO, THE ROAD LEADING TO THE CENTRE IS NOT MOTORABLE
AGRIC	NRCRI, IMUDIKE	COMPLETION OF CONSTRUCTION OF CASSAVA PROCESSING CENTRE AT EZUHU, UMUNA, ONUIMO, IMO STATE	20,000,000	DONE	THOUGH IMPLEMENTED, THIS PROJECT LOOKS ABANDONED - ONLY SOME OUTER PART OF THE CENTRE CAN BE SEEN. HOODLUMS NOW OCCUPY THE SITE, WITH UNWHOLESOME ACTIVITIES PREVALENT
INFORMATION		LIABILITY FOR BRIX DEVELOPMENT FOR CAPACITY TRAINING FOR IMO STATE JOURNALISTS	35,000,000	NOT DONE	PROJECT NOT IMPLEMENTED

MINISTRY	AGENCY	PROJECT TITLES	AMOUNT	STATUS	OBSERVATION
INFORMATION	HEARTLAND FM, OWERRI	COMPLETION AND FURNISHING OF OFFICE COMPLEX	70,000,000	COMPLETED	COMPLETED AND IN FULL OPERATION
HEALTH	FMC, OWERRI	OUTSTANDING LIABILITY FOR THE FREE EYE SCREENING PROGRAMME	20,000,000	NOT DONE	WE REPORT THAT THE PROJECT IS KNOWN BUT HAS NOT BEEN IMPLEMENTED; THE HEAD OF THE RELEVANT DEPARTMENT WAS NOT PRESENT FOR QUESTIONING AS AT THE TIME OF TRACKING
SPORT	SPORT	COMPLETION OF CONSTRUCTION OF MBUTU GRAND STAND (MINI STADIUM) ABOH MBAISE, IMO STATE	35,000,000	ABANDONED	THE STADIUM IS SITUATED IN A SCHOOL FIELD WHERE STUDENTS GO TO REST DURING BREAK AND AFTER SCHOOL
POLICE FORMATION	POLICE FORMATION	COMPLETION OF CONSTRUCTION OF MBUTU POLICE STATION	25,000,000	COMPLETED	PROJECT IMPLEMENTED
TRADE	SMEDAN	SUPPLY OF KEKE NAPEP FOR ECONOMIC EMPOWERMENT PROGRAMME IN ORLU/ORSU/ORU-EAST FEDERAL CONSTITUENCY, IMO STATE	60,000,000	NOT DONE	PROJECT LOCATION IS UNKNOWN
WATER	AIRBA	CONSTRUCTUION OF 500 KVA TRASNFORMER SUBSTATIONS FOR OWERRI FEDERAL CONSTITUENCY, IMO STATE	20,000,000	NOT DONE	PROJECT LOCATION IS UNKNOWN
WATER	AIRBA	CONSTRUCTION OF SOLAR BOREHOLES FOR OWERRI FEDERAL CONSTITUENCY, IMO STATE	20,000,000	NOT DONE	PROJECT LOCATION IS UNKNOWN
TRADE	SMEDAN	CONSTRUCTION OF MODERN DAILY MARKET AT ARONDIZUOGU IN IDEATO, IDEATO NROTH FEDERAL CONSTITUENCY, IMO STATE	40,000,000	COMPLETED	PROJECT IMPLEMENTED, BUT NOTED AS QUITE FAR FROM WHERE COMMUNITY MEMBERS LIVE
TRADE	SMEDAN	CONSTRUCTION O FO PRIMARY HEALTH CARE CENTRE AT IKPEZE, IDEATO NORTH FEDERAL COSNTITUENCY OF IMO STATE	20,000,000	COMPLETED	PROJECT IMPLEMENTED BUT NOT YET IN USE
POWER	REA	PROVISION AND INSTALLATION OF TRANSFORMERS AND POLES IN AJABO/UMUNA ONUIMO LGA, IMO STATE	20,000,000	NOT COMPLETED	THIS PROJECT WAS NOT IMPLEMENTED, WITH COMMUNITY MEMBERS STATING THEY NEED ELECTRICITY AS WELL AS OTHER BASIC AMENITIES
POWER	REA	PROVISION AND INSTALLATION OF TRANSFORMERS AND POLES IN EZELU OKWE ONUIMO LGA, IMO STATE	20,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
POWER	REA	COMPLETION OF RURAL ELECTRIFICATION OF OBOHIA AND ERU AUT. COMMUNITIES, AHIAZU - MBAISE, IMO STATE	25,000,000	ONGOING	ORU (NOT ERU AS SEEN IN BUDGET) HAS BEEN ELECTRIFIED; MEANWHILE, OBOHIA IS ONLY JUST BEING ELECTRIFIED
WATER	AIRBA	COMPLETION OF WATER PROJECTS AT DERIE-IHITTE, UMUORE, OKIRIKA - NWEKE, EBODO - UJICHI, UMUAWADA, AGUNEZE IN AHIZU FEDERAL CONSTITUENCY, IMO STATE	10,000,000	NOT DONE	NO WATER PROJECTS EXIST AND RESIDENTS ARE UNAWARE OF THE PROJECT
WATER	AIRBA	CONSTRUCTUION OF SOLAR POWERED BOREHOLE AND RETICULATION IN AZARA OBIATO, ALENYI OGWA, AMUCHA AUTONOMOUS COMMUNITY AND OHAOHIA OBI MBIERI MBAITOLI, IMO STATE	10,000,000	NOT DONE	COMMUNITY MEMBERS ARE NOW AWARE OF THIS PROJECT, WHICH HAS NOT BEEN IMPLEMENTED
LANDS	LANDS	CONSTRUCTION OF 80 MARKET STALLS AT ORIE AMAIGWE MARKET, UMUNOHA AND NKWO ORODO MARKET IN MBAITOLI LGA, IMO STATE	15,000,000	NOT DONE	THE STALLS CURRENTLY IN USE ARE THOSE BUILT 4 YEARS AGO BY THE PAST GOVERNMENT

MINISTRY	AGENCY	PROJECT TITLES	AMOUNT	STATUS	OBSERVATION
WATER	AIRBA	COMPREHENSIVE RENOVATION OF SIX CLASSROOM BLOCK AT GROUP SCHOOL MBUTU NWORIE, ABOH MBAISE, IMO STATE	30,000,000	COMPLETED	PROJECT NOT FULLY IMPLEMENTED; THOUGH STATED AS A 6-BLOCK CLASSROOM, WE REPORT WHAT IS ON THE GROUND IS A 5-BLOCK CLASSROOM
WATER	AIRBA	STUDY FOR THE CONTROL OF UMULOLO-OKOROKA-UMUOKISI EROSION/FLOOD CONTROL PROJECT, NGURU NWENKWO, ABOH MBAISE, IMO STATE	30,000,000	ONGOING	WORK IS JUST COMMENCING, AS CONTRACTORS AND ENGINEERS HAVE ARRIVED ONSITE
SGF	NAPEP	MULTIPURPOSE CIVIC CENTRE AT OMUMA, ORU EAST LGA, IMO WEST SENATORIAL DISTRICT, IMO STATE	80,000,000	NOT DONE	PROJECT NOT IMPLEMENTED; THE COMMUNITY RULER REPORTS THAT THE PROJECT IS UNHEARD OFF IN THE CONSTITUENCY
SGF	NAPEP	REHABILITATION OF OMUMA MODERN MARKET ORU EAST LGA, IMO STATE	53,000,000	NOT DONE	THIS PROJECT WAS NOT IMPLEMENTED; THE MARKET DOES NOT LOOK MODERN, AND THERE IS NO REHABILITATION ONGOING

ONDO STATE

NO. OF PROJECTS TRACKED	COMPLETED	ONGOING	NOT DONE
33	14	3	16

tracka
www.tracka.ng

SAMPLE PROJECTS

PROJECT: Renovation of L.A Primary School, Oloruntedo, Ward 4, Ondo West Senatorial District

COST: N5.5 million

This project was yet to commence at the time of project tracking. PTOs visited the community in May 2016 and discovered firsthand that some pupils were heading to farms during school hours. Further inquiries saw residents report that the dilapidated building has forced many pupils out of schooling, making many resort to farming in the interim. PTOs also noted that a set of new chairs was supplied to the school, despite the absence of actual classrooms for pupils to sit in.

PROJECT: Provision of Solar Street Light in Isuwada Road via Oluata Street, Owo, Ondo State

COST: N15 million

Tracka's PTOs report that this project has

been completed. According to the constituents, the illumination of the streets at night has reduced crime around the area. However, some community members noted that the solar lamps could be substandard products, and had to be engaged by PTOs on the fact that this particular claim could not be immediately ascertained just by a cursory examination of the lamps.

PROJECT: Completion of the Construction of Medium Basic Health Centres in Akindana/Atosin

COST: N8 million

This project is classified as implemented. Akindana and Atosin are two communities that share a border. Residents asserted that prior to the construction of the new medical centers, pregnant women and others in need of medical attention in both communities had to travel 15 km to Idanre town. Stakeholders reported to PTOs that the

newly-built centers will reduce maternal and infant mortality as well as bring development to both communities.



*Medium Basic Health Centres in
Akindana/Atosin*

PROJECT: Building of Civic Centre at Igbotako in Okitipupa LGA
COST: N25 million

Fieldwork by PTOs revealed that the Civic center was yet to be built. Residents also expressed disapproval of the project and suggested that the funds should instead have been diverted to the rehabilitation of dilapidated school buildings in the community.

MINISTRY	AGENCY	PROJECT TITLES	AMOUNT	STATUS	OBSERVATION
WOMEN	NCWD	MOTOCYCLE SUPPLY IN IDANRE/IFEDORE FEDERAL CONSTITUENCY	55,000,000	NOT DONE	PROJECT NOT IMPLEMENTED AS AT TIME OF VISIT
WOMEN	NCWD	SUPPLY OF MOTORCYCLES TO THE YOUTHS OF AKOKO N.E./AKOKO N.W FEDERAL CONSTITUENCY	55,000,000	NOT DONE	PROJECT NOT IMPLEMENTED; COMMUNITY MEMBERS REPORT THAT DISTRIBUTING MOTORCYCLES IS NOT THE BEST WAY TO ALLEVIATE POVERTY, AS THIS IS NOT SUSTAINABLE
EDUCATION	UBEC	RENOVATION OF L.A PRIMARY SCHOOL, OLORUNTEDO WARD 4, ONDO WEST	5,500,000	ONGOING	THE SCHOOL IS STILL DILAPIDATED, DESPITE SOME WORK ONGOING
SCIENCE	PRODA	STRATEGIC INTERVENTION	50,000,000	NOT DONE	THIS PROJECT IS NOT TRACEABLE, WITH THE COMMUNITY OR LOCAL GOVERNMENT UNABLE TO CLARIFY AS THEY ARE UNAWARE OF ITS EXISTENCE
LABOUR	LABOUR	EMPOWERMENT AND TRAINING OF YOUTHS ON LIVESTOCK AND PROVISION OF STARTER PACKS IN AKOKO SOUTH WEST/SOUTH EAST LGAs	55,500,000	NOT DONE	PROJECT NOT IMPLEMENTED
SGF	BCDA	SUPPLY OF MOTOR CYCLES TO AKURE NORTH/SOUTH FEDERAL CONSTITUENCY	25,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
SGF	BCDA	SUPPLY OF MOTOR CYCLES TO AKURE NORTH/SOUTH FEDERAL CONSTITUENCY	30,000,001	NOT DONE	THIS PROJECT WAS NOT IMPLEMENTED; QUANTITIES OR BENEFICIARIES COULD NOT BE ASCERTAINED
WOMEN	NCWD	SUPPLY OF TRICYCLES TO IDASHEN OWO LGA	55,000,000	NOT DONE	THIS PROJECT WAS NOT IMPLEMENTED
TRADE	SMEDAN	STRATEGIC EMPOWERMENT PROGRAMME FOR SUPPLY OF TRICYCLES AND MOTORCYCLES	55,500,000	NOT DONE	THIS BUDGETARY ITEM WAS NOT DEFINED
YOUTH	YOUTH	BUILDING OF CIVIC CENTRE AT IGBOTAKO IN OKITIPUPA LGA	25,000,000	NOT DONE	THIS PROJECT WAS NOT IMPLEMENTED; RESIDENTS REPORT THEY WOULD PREFER MEASURES THAT CURB RURAL-URBAN MIGRATION INSTEAD
YOUTH	YOUTH	BUILDING OF CIVIC CENTRE AT IRELE IN IRELE LGA	30,000,000	NOT DONE	PROJECT NOT IMPLEMENTED; A CIVIC CENTRE ALREADY EXISTS, BUILT IN 2012. RESPONDENTS SUGGEST THIS IS A REDUNDANT PROJECT RE-ADDED TO THE BUDGET
EDUCATION	UBEC	CONSTRUCTION OF 3 BLOCKS OF CLASSROOM IN ONDO NORTH SENATORIAL DISTRICT, ONDO STATE	30,000,000	DONE	PROJECT IMPLEMENTED
ENVIRONMENT	ENVIRONMENT	EROSION CONTROL IN OKITIPUPA AND IRELE LGA, ONDO SOUTH SENATORIAL DISTRICT, ONDO STATE.	61,000,000	NOT DONE	PROJECT NOT IMPLEMENTED; WE WERE UNABLE TO FIND A LOCATION NEEDING EROSION CONTROL IN THIS CONSTITUENCY.
HEALTH	NHIS	COMPLETION OF THE CONSTRUCTION OF MEDIUM BASIC HEALTH CENTRES PROJECTS IN OWENA AKINDANA/ATOSIN IDANRE IN ONDO CENTRAL SENATORIAL DISTRICT, ONDO STATE.	8,000,000	DONE	PROJECT IMPLEMENTED
HEALTH	NHIS	COMPLETION OF THE CONSTRUCTION OF MEDIUM BASIC HEALTH CENTRES PROJECTS IN APONMU-LONA IDANRE IN ONDO CENTRAL SENATORIAL DISTRICT, ONDO STATE.	8,000,000	NOT DONE	WE REPORT THAT LAND DISPUTES HAVE FORCED A DELAY IN THIS PROJECT, HALTING ITS IMPLEMENTATION

MINISTRY	AGENCY	PROJECT TITLES	AMOUNT	STATUS	OBSERVATION
LABOUR	NDE	SUPPLY OF TRICYCLES AND TAILORING EQUIPMENTS FOR EMPOWERMENT OF YOUTHS AND WOMEN IN ONDO CENTRAL SENATORIAL DISTRICT, ONDO STATE	20,000,000	DONE	PROJECT IMPLEMENTED
LABOUR	NDE	SUPPLY OF MOTORCYCLES FOR EMPOWERMENT OF YOUTHS IN ONDO CENTRAL SENATORIAL DISTRICT, ONDO STATE	75,000,000	DONE	PROJECT IMPLEMENTED
SCIENCE	ENERGY COMM	PROVISION OF SOLAR STREET LIGHT IN ISUWADA ROAD VIA OLUATA STREET, OWO, ONDO STATE	15,000,000	DONE	PROJECT IMPLEMENTED; HOWEVER, THE QUALITY OF WORK BY THE ENERGY COMMISSION IS WORRISOME
SCIENCE	ECN	PROVISION OF 80 NOS. SOLAR STREET LIGHT POLES IN ONDO NORTH SENATORIAL DISTRICT, ONDO STATE	61,000,000	DONE	MOST RECIPIENT COMMUNITIES ENJOY IMPLEMENTATION OF THIS PROJECT BUT RESIDENTS FEEL THE WORK IS SUBSTANDARD AND MAY NOT LAST
LABOUR	LABOUR	EMPOWERMENT AND TRAINING OF YOUTHS ON LIVESTOCK AND PROVISION OF STARTER PACKS IN AKOKO SOUTH WEST/SOUTH EAST LGAs	55,500,000	NOT DONE	PROJECT NOT IMPLEMENTED
SCIENCE	ECN	PROVISION OF 3NOS. SOLAR POWERED BOREHOLES IN ONDO NORTH SENATORIAL DISTRICT, ONDO STATE	20,000,000	DONE	PROJECT NOT IMPLEMENTED
WATER	OGUN/ OSUN	PROVISION OF SOLAR POWERED BOREHOLE AT UKA STREET IN OWOW , IN ONDO STATE	15,000,000	DONE	PROJECT IMPLEMENTED
WOMEN	NDE	SUPPLIES OF MOTORCYCLES, SEWING MACHINES, HAIR DRESSING DRIERS, GENERATIING SETS, AND CLIPPERS AND OTHER EMPOWERMENT MATERIALS FOR ONDO SOUTH SENATORIAL DISTRICT, ONDO STATE.	50,000,000	NOT DONE	PROJECT NOT IMPLEMENTED; ALSO, MOST ARTISANS REPORT LOW PATRONAGE

KANO STATE

NO. OF PROJECTS TRACKED	COMPLETED	ONGOING	NOT DONE
39	4	3	32

tracka
www.tracka.ng

PROJECT: Construction and equipping of e-learning center in Kano North Senatorial District

COST: 221.94 million

As at time of visit, the Tracka team discovered that construction of the e-learning center was yet to commence. The sole structure at the site was the Rural Information Technology Center (R.I.T.C), which was built in 2014 but has remained unused, due to lack of necessary equipment. Constituents told PTOs that their wish is the full delivery of the e-learning centers as this will not only assist in the education and training of many youths in the Kano North Senatorial district but the venue also serve as a computer-based facility for examinations such as the university entrance test popularly called JAMB.

PROJECT: Construction of 2 units of two (2) blocks of three (3) classrooms at Dakata and Tudun Murtala wards in Nassarawa LGA Kano State

COST: N20 million

Our tracking officers made repeated visits to Dakata and Tudun Murtala School in Nassarawa LGA, the last of which was recorded in May 2016. The findings showed that this project is yet to be completed. PTOs' first visit to the project site was in February 2016, and upon extensive engagement, the legislative Representative for the community promised to facilitate execution of the project.

Subsequent visits showed only one block of 2 classrooms was built at Dakata secondary school, as opposed to the 2 block description stated in the budget. The existing classes in the other block are in a deplorable state and there is an urgent need for rehabilitation of the entire educational facility.



Govt. Senior Islamic Sec. School, Dakata

PROJECT: Construction of Dutsen Bakoshi Dam/Gezawa in Shanono and Tsanyawa LGAs in Kano North Senatorial District (ongoing)

COST: N98 million

As at May 2016, PTOs report that this dam had not been constructed. However, there is an existing dam constructed in 2013, which however possesses scant capacity to meet the needs of the communities in this constituency.

According to residents, they are in dire

need of the new dam to support irrigation and other domestic needs of the populace.

PROJECT: Construction of Gaya-Balare Road, Kano State

COST: 20 million

Balare has one of the biggest markets in the Kano south senatorial district. To access the market, people must use an alternate road in an area called Ajingi. PTOs also noted that this road was yet to be constructed as at the time of visit in February 2016.

MINISTRY	AGENCY	PROJECT TITLES	AMOUNT	STATUS	OBSERVATION
	EDUCATION	COMPLETION OF THE RENOVATION OF DEMONSTRATION STAFF SCHOOL AT BAYERO UNIVERSITY SCHOOL, KANO	35,000,000	NOT DONE	AUTHORITIES OF THE SCHOOL REPORT THEY ARE UNAWARE OF THIS PROJECT
	EDUCATION	COMPLETION OF UPGRADING SCHOOL OF UNDERGRADUATE STUDIES AT BAYERO UNIVERSITY, KANO STATE	15,000,000	NOT DONE	PROJECT STATUS UNCLEAR AS NO SCHOOL OF UNDERGRADUATE STUDIES EXISTS
	FRSC	CONSTRUCTION OF FOUR SECTOR OFFICES AT KANO, KEBBI, OSHOGBO AND ABAKALIKI AT N125m EACH	500,000,000		PROJECT NOT IMPLEMENTED
	POLICE FORMATION	SUPPLY AND INSTALLATION OF 92 STAND-ALONE SOLAR STREET LIGHT AT POLCE ACADEMY (POLAC) WUDIL, KANO STATE. (OUTSTANDING LIABILITY)	43,000,000	COMPLETED	PROJECT HAS BEEN IMPLEMENTED
	WOMEN	WOMEN EMPOWERMENT SEWING MACHINE RANO/BUNKURE/KIBIYA KANO STATE	20,000,000	COMPLETED	PROJECT NOT IMPLEMENTED
	NPHCDA	DELIVERY OF FREE MATERNAL CHILD AND OTHER HEALTH SEERVICES IN SUMAILA LGA KANO STATE	20,000,000	NOT DONE	COMMUNITY MEMBERS APPEALED FOR IMPLEMENTATION OF THE PROJECT
	HJRBDA	CONSTRUCTION OF HANDPUMPS BOREHOLE IN GWARZO/KABO FED CONST KANO STATE	20,000,000	NOT DONE	PROJECT NOT IMPLEMENTED.
	WOMEN	SUPPLY OF GENERATOR SET TO KARAYE/ROGO KANO STATE	20,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
	NDE	1 SEATER BUS TYPE B. (FOR GIRL'S DAY STUDENT TRANSPORT ASSISTANCE IN FAGGE,KANO STATE	10,000,000	NOT DONE	PROJECT NOT IMPLEMENTED.
	NDE	100 NO LIPAN MOTOR CYCLE FOR YOUTH EMPOWERMENT IN FAGGE,KANO STATE	10,000,000	DONE	REPORTS INDICATES ONLY 20 PEOPLE BENEFITTED FROM THIS PROJECT
	SMEDAN	STRATEGIC EMPOWERMENT PROGRAMME FOR GWALE FED CONST KANO STATE	20,000,000	NOT DONE	PROJECT NOT IMPLEMENTED.
	SMEDAN	STRATEGIC EMPOWERMENT PROGRAMME FOR GWALE FED CONST KANO STATE	20,000,000	NOT DONE	PROJECT NOT IMPLEMENTED.
	NCWD	WOMEN EMPOWERMENT SEWING MACHINES BICHI FED CONST KANO STATE	10,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
	NCWD	YOUTH EMPOWERMENT TRICYCLES BICHI FED CONST KANO STATE	10,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
	YOUTH	SUPPLY OF MOTORCYCLES AT DAWAKIN-TOFA/RIMINGADO/TOFA FED CONST KANO STATE	20,000,000	DONE	STALLS IN USE ARE THOSE BUILT 4 YEARS AGO BY PAST GOVERNMENT
	REFUGEES	SUPPLY OF MOTORCYCLES DANBATTA/MAKODA KANO STATE	20,000,000	DONE	PROJECT IMPLEMENTED ONLY IN DANBATTA; REPORTS ALSO STATE BENEFICIARIES WERE FEW
	NCWD	SUPPLY OF MOTORCYCLES IN TSANYAWA/KUNCHI KANO STATE	20,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
	REFUGEES	SUPPLY OF MOTORCYCLES KANO MUNICIPAL KANO STATE	20,000,000	NOT DONE	RESPONDENTS FEEL PROJECT HAS NO ECONOMIC VALUE AS MOTORCYCLE RIDERS ARE BANNED FROM THE METROPOLIS BY GOVERNMENT

MINISTRY	AGENCY	PROJECT TITLES	AMOUNT	STATUS	OBSERVATION
	UBEC	CONSTRUCTION OF 2 UNIT OF TWO (2) BLOCKS OF THREE (3) CLASSROOMS AT DAKATA & TUDUN MURTALA WARDS IN NASARAWA LGA KANO STATE @ N10,000,000 EACH.	20,000,000	DONE	ONLY ONE CLASSROOM BLOCK CONSTRUCTED AT DAKATA SECONDARY SCHOOL AS AT TIME OF VISIT
	SMEDAN	SUPPLY OF 119 UNITS OF MOTORCYCLES IN TARAUNI, KANO STATE	15,000,000	DONE	ACCOUNTS FROM RESIDENTS STATE ONLY TWO MOTORCYCLES DISTRIBUTED; SCHEME TERMED REDUNDANT AS MOTORCYCLE RIDERS ARE BANNED IN THE STATE
	SMEDAN	SUPPLY OF 92 UNITS OF GRINDING MACHINE IN TARAUNI, KANO STATE	5,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
	NDE	TRAINING AND EMPOWERMENT OF YOUTH AND WOMEN IN MINJIBIR/UNGOGO FED CONST KANO STATE	20,000,000	NOT DONE	COMMUNITY MEMBERS REPORT THEY WOULD PREFER ROADS, SCHOOLS AND HEALTHCARE RATHER THAN THIS UNIMPLEMENTED PROJECT
	ECN	PROVISION OF SOLAR STREET LIGHTS IN DOGUWA/TUDUNWADA FED CONST KANO STATE	20,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
	WOMEN	SEWING AND EMBROIDERY MACHINES THROUGH YOUTH AND WOMEN EMPOWERMENT AT DAWAKINKUDU/WARAWA FED CONST KANO STATE	10,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
	WOMEN	GRINDING MACHINES THROUGH YOUTH AND WOMEN EMPOWERMENT AT DAWAKINKUDU/WARAWA FED CONST KANO STATE	10,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
	REFUGEES	PROVISION OF MOTOR CYCLES IN DALA FED CONST KANO STATE	15,000,000	NOT DONE	NO ECONOMIC VALUE BECAUSE THE GOVERNMENT HAS BANNED OKADA IN THE METROPOLIS
	REFUGEES	SEWING MACHINE IN DALA FED CONST KANO STATE	5,000,000	NOT DONE	PROJECT IMPLEMENTATION WOULD LEAD TO POSITIVE IMPACT
	NCWD	YOUTH EMPOWERMENT PURCHASE OF TRICYCLES IN GEZAWA/GABASAWA IN KANO STATE	20,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
	HJRBD	HANDPUMP BOREHOLES AT BAGWAI/SHANONO FED CONST OF KANO STATE	20,000,000	NOT DONE	THE COMMUNITIES ARE IN NEED OF BOREHOLES
	YOUTH	15 NOS HANDPUMPS IN VARIOUS LOCATION OF MADOBI LGA KANO STATE	20,000,000	NOT DONE	REPORTS SUGGEST THAT RATHER THAN GOVERNMENT, UNICEF AND DANGOTE PLC ARE ORGANISATIONS THAT DRILLED BOREHOLES IN MADOBI
	HUMAN RIGHT	ADVOCACY AND SENSITIZATION IN GARKO LGA KANO STATE	20,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
	LANDS	CONSTRUCTION OF GAYA-BALARE ROAD KANO STATE	20,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
	SMEDAN	SUPPLY OF UNITS OF MOTORCYCLES TO KIRU/BEBJI FED CONST KANO STATE	20,000,000	DONE	ONLY 15 DISTRIBUTED IN KIRU AND 14 IN BEBEJI; THE PEOPLE STATE THEY NEED ROADS AND SCHOOLS RENOVATED
	AGRIC	YOUTH AND WOMEN EMPOWERMENT IN AGRO PROCESSING IN KUMBOTSO FED CONST KANO STATE	20,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
	EDUCATION	COMPLETION AND FURNISHING OF INTERNATIONAL CONFERENCE CENTRE AT BAYERO UNIVERSITY, KANO (ON GONG)	436,560,000	ONGOING	PROJECT NOT IMPLEMENTED
	SGF	RE-INTERGRATION OF INTERNALLY DISPLACED PERSONS IN KANO SOUTH SENATORIAL DISTRICT, KANO STATE.	85,000,000	NOT DONE	PROJECT NOT IMPLEMENTED

OYO STATE

NO. OF PROJECTS TRACKED	COMPLETED	ONGOING	NOT DONE
26	7	7	12

tracka
www.tracka.ng

SAMPLE PROJECTS

PROJECT: Rehabilitation of Otu-Ipapo Road, Itesiwaju LGA
COST: N50 million

The Tracka team gathered from physical research and fact checks that the Otu-Ipapo road was constructed in 2014. As part of some zonal intervention projects, N50mn was allocated for the rehabilitation of the newly constructed Otu-Ipapo road in 2015.

This was executed, but the road still has potholes, with a poor drainage system causing more damage to the project. This suggest the possibility that the construction and rehabilitation of the road were all shabbily carried out and there was little or no monitoring during the execution of both project actions to ensure quality control.



Rehabilitation of Otu-Ipapo Road, Itesiwaju LGA

PROJECT: Completion of Flood and Erosion Control at Isale Ifon Allo
COST: N66 million

The Tracka team met with the site engineer at the flood and erosion control project site; he reported that the first phase of the project had been completed though there were laborers working on sand-filling some parts of the site. During the second visit, it was discovered that both engineers and laborers were absent from their workstations and work had been invariably halted.

PTOs subsequently engaged with the community about the project and were informed that the erosion control aspect was to be done from Isale-Ifon all through until Ikuye but work only done in easily noticed areas. A call was placed to the site engineer to query abandonment of the project, and he stated this project will proceed whenever the client asks them to continue.



Completion of Flood and Erosion Control at Isale Ifon Allo

PROJECT: Power Improvement from Navy School, Iresaapa to Idi-Opele and Iranyi Township, all in Surulere LGA

COST: N30 million

Research on this project revealed that electric poles and wires were installed from Navy school, Iresaapa to Idi-Opele.

PTOs' visit to Idi-Opele town also showed that though the electric poles and wires were fixed, other necessary installations like power lines were yet to be implemented. Therefore the affected communities have not enjoyed power supply.

Further investigation by PTOs on a visit to Iranyi town revealed a lack of electricity also exists in this location, due to the absence of electric poles and wires in the town. According to the respondents, the tardiness on this project has caused low productivity for the farming populations, as agricultural output and associated raw

materials could not be processed due to non-existent power supply.

PROJECT: Construction of 1 Block of 3 Classrooms with furniture & Vocational and Entrepreneurship Centre, Okaka Federal College of Animal Health and Production (Itesiwaju LGA)

COST: N15 million

The one block 3-classroom project was tracked to an isolated area along Iseyin-saki road. The building looked abandoned, with bushes growing around its perimeter. Though construction (building and roofing) have been carried out, the structure was yet to be finished off - painting, electrical fittings, and other necessities. A subsequent visit was paid to the site by PTOs in May 2016 and we report that no signs of continuation on the project was recorded.



Vocational and Entrepreneurship Centre, Okaka Federal College of Animal Health and Production (Itesiwaju LGA)

MINISTRY	AGENCY	PROJECT TITLES	AMOUNT	STATUS	OBSERVATION
WATER	OORBDA	COMPLETION OF AJINAPA WATER SUPPLY SCHEME AT ORIRE LG, OYO STATE	196,000,000	ONGOING	WORK IS ALMOST COMPLETED
WATER	LNRBDA	EROSION AND FLOOD CONTROL FOR OGBOMOSHO SOUTH LGA OF OYO STATE	51,000,000	COMPLETED	PROJECT IMPLEMENTED
WATER	OORBDA	PROVISION OF BOREHOLES AT OGBOMOSHO NORTH, SOUTH AND ORIRE FEDERAL CONSTITUENCY, OYO STATE	146,000,000	NOT DONE	REPORTS FROM VARIOUS SOURCES INDICATE THIS PROJECT REMAINS UNIMPLEMENTED
EDUCATION	UBEC	CONSTRUCTION OF TWO CLASSROOM BLOCKS WITH TOILETS AND OFFICE AT OGBOMOSHO NORTH LGA, OYO	16,000,000	COMPLETED	CLASSROOM BLOCKS HAVE BEEN CONSTRUCTED; SCHOOL AUTHORITIES REPORT THEY ARE YET TO BE GRANTED ACCESS TO THE FACILITY
EDUCATION	UBEC	CONSTRUCTION OF TWO CLASSROOM BLOCKS WITH TOILETS AND OFFICE AT OGBOMOSHO SOUTH LGA, OYO	16,000,000	NOT DONE	PROJECT NOT YET IMPLEMENTED
EDUCATION	UBEC	CONSTRUCTION OF TWO CLASSROOM BLOCKS WITH TOILETS AND OFFICE AT ORIRE LGA, OYO STATE	16,000,000	COMPLETED	BUILDING COMPLETED; SCHOOL PRINCIPAL HOWEVER REPORTS THE AVAILABLE CLASSROOMS ARE INSUFFICIENT TO SERVE STUDENTS
POWER	NREA	RURAL ELECTRIFICATION IN 6 AREAS AT OGBOMOSHO NORTH, SOUTH AND ORIRE FEDERAL CONSTITUENCY, OYO	96,000,000	NOT DONE	NO TRACES OF ELECTRIFICATION IN THIS CONSTITUENCY. COMMUNITY HEADS AND MEMBERS STRONGLY EXPRESSED THEIR DISPLEASURE OVER NON-IMPLEMENTATION
WATER	LNRBDA	COMPLETION OF FLOOD AND EROSION AT ISALE IFON IN OGBOMOSHO NORTH, OYO STATE	66,000,000	ONGOING	ABANDONED PROJECT
SCIENCE	ECN	COMPLETION OF SOLAR STREET LIGHTS AND BOREHOLES AT OGBOMOSHO NORTH, SOUTH AND ORIRE FEDERAL CONSTITUENCY, OYO STATE	41,000,000	NOT DONE	PROJECT NOT IMPLEMENTED
POWER	NREA	COMPLETION OF RURAL ELECTRIFICATION AT OLORUNDA, ORIRE LG, OYO STATE	6,000,000	ONGOING	ELECTRIC POLES AND WIRES LAID, BUT POWER LINES AND FURTHER INSTALLATION YET TO BE FIXED. PROJECT ABANDONED
ENVIRONMENT	ENVIRONMENT	PROVISION OF WATER AND ELECTRIFICATION AT RECREATION PARK AT ORIRE LG, OYO STATE	6,000,000	COMPLETED	PROJECT IMPLEMENTED
POWER	NREA	PURCHASE AND INSTALLATION OF TRANSFORMERS AT OGBOMOSHO NORTH, SOUTH AND ORIRE FEDERAL CONSTITUENCY, OYO STATE	46,000,000	NOT DONE	PROJECT HAS NOT BEEN IMPLEMENTED
WATER	OORBDA	WATER SUPPLY SCHEME AT OKO, SURULERE LG, OYO STATE	46,000,000	ONGOING	THE WATER SCHEME IS NOTED AS ONGOING
TRADE	SMEDAN	SUPPLY OF POVERTY ALLEVIATION MATERIALS FOR CONSTITUENTS OF IBADAN NORTH EAST AND SOUTH EAST FED. CONSTITUENCY	10,785,714	NOT DONE	PROJECT NOT IMPLEMENTED
EDUCATION	UBEC	CONSTRUCTION OF 2 CLASSROOMS WITH FURNITURE @ ANGLICA - METHODIST SECONDARY SCHOOL, OYO, OYO EAST LGA	15,000,000	COMPLETED	CLASSROOMS BUILT; BUT SCHOOL OFFICIALS REPORT THEY HAVE NO ACCESS TO THE PROJECTS

MINISTRY	AGENCY	PROJECT TITLES	AMOUNT	STATUS	OBSERVATION
LABOUR	NDE	PROVISION OF POVERTY ALLEVIATION MATERIALS AT IREPO/OORELOPE LG, OYO STATE	16,000,000	COMPLETED	RESIDENTS CONFIRMED THE AWARENESS OF THE PROGRAM
TRADE	SMEDAN	SUPPLY OF TRICYCLES AND MOTORCYCLES AT IBARAPA EAST/IDO FEDERAL CONSTITTUENCY, OYO STATE	11,000,000	NOT DONE	THE PROJECT IS NOT DONE AND MOST OF PREVIOUS ONES HAS NO BASIS OF THE SELECTING THE BENEFICIARIES, ALSO THE TRICYCLES WERE SHARED TO RULING PARTY MEMBER AND NOT TO GENERAL COMMUNITY
WATER	LNRBDA	HAND PUMP BOREHOLES IN VARIOUS VILLAGES IN OYO FEDRAL CONSTITTUENCY, OYO LGA	21,000,000	ONGOING	THE CONSTRUCTION OF HAND PUMP BOREHOLES STILL CONTINUES WHILE SOME AREAS HAS BEEN COMPLETED
SGF	NACA	HIV AWARENESS CAMPAIGN AND FREE MEDICAL MISSION OUTREACH OLUYOLE LGA	24,000,000	COMPLETED	PROJECT HAS BEEN IMPLEMENTED
SGF	NACA	HIV AWARENESS CAMPAIGN AND FREE MEDICAL MISSION AT HEALTH CENTRE ODO ONA ELEWE OLUYOLE LGA	12,000,000	COMPLETED	THERE IS MORE NEED TO SENSITIZE PEOPLE WITH HIV POSITIVE ON HOW TO DEAL WITH STIGMATIZATION
LABOUR	NDE	CONSTRUCTION OF A BLOCK OF 3 CLASSROOMS WITH FURNISHING + VIP TOILET AT NAWAR-UD-DEEN SECONDARY SCH,SANNGO SAKI	12,000,000	COMPLETED	COMPLETED BUT THE CHALK BOARD AND WATER SYSTEM IS YET TO BE FIXED FOR BOTH THE CLASSROOMS AND TOILETS
TRADE	TRADE	ICT INFRASTRUCTURE AND CENTRES AT EGBEDA AND ONA -ARA LGAs	36,000,000	NOT DONE	PROJECT HAS NOT BEEN IMPLEMENTED
TRADE	SMEDAN	STRATEGIC EMPOWERMENT PROGRAMME FOR IBARAPA EAST/IDO FED. CONSTITTUENCY	35,785,714	NOT DONE	NO EVIDENCE TO ASCERTAIN IMPLEMENTATION; RESPONSES INDICATE THIS PROGRAMME IS PERCEIVED AS A MEDIUM FOR LOOTING PUBLIC FUNDS
TRADE	TRADE	SUPPORT FOR ICT INFRASTRUCTURE AT OGBOMOSHO NORTH, SOUTH AND ORIRE FEDERAL CONSTITTUENCY, OYO STATE	6,000,000	NOT DONE	PROJECT ONLY SEEN AT IKOYI GRAMMAR SCHOOL ORIIRE LGA - NONE SEEN AS IMPLEMENTED IN OTHER AREAS
TRADE	TRADE	INDUSTRIAL DATA BANK UPGRADE AT OGBOMOSHO NORTH, SOUTH AND ORIRE FEDERAL CONSTITTUENCY, OYO STATE	16,000,000	NOT DONE	COMMUNITY MEMBERS REPORT THIS EXERCISE WAS IMPLEMENTED, AND WISH IT WOULD OCCUR PERIODICALLY
SGF	NACA	HIV AWARENESS CAMPAIGN AND FREE MEDICAL MISSION OUTREACH AT OROGUN, AKINYELE LGA	16,500,000	COMPLETED	COMMUNITY MEMBERS REPORT THIS EXERCISE WAS IMPLEMENTED, AND WISH IT WOULD OCCUR PERIODICALLY
SGF	NACA	HIV AWARENESS CAMPAIGN AND FREE MEDICAL MISSION OUTREACH AT ABIDIODAN IN LAGELU LGA	16,000,000	COMPLETED	PROGRAMME IMPLEMENTED
WATER	LNRBDA	COMPLETION OF EROSION CONTROL PROJECT IN OJA TITUN AREA OF KISI, IREPO LGA	11,500,000	COMPLETED	COMMUNITY REPORTS PROJECT WAS IMPLEMENTED BUT SAY SOME AREAS WERE LEFT UNTOUCHED
LABOUR	NDE	PURCHASE AND SUPPLY OF POVERTY ALLEVIATION ITEMS TO IREPO LGA	23,500,000	COMPLETED	REPORTS INDICATE THE ELECTED REPRESENTATIVE RANDOMLY SELECTED BENEFICIARIES, AS OPPOSED TO TARGETING THE GENERAL COMMUNITY
TRADE	SMEDAN	TRAINING AND EMPOWERMENT OF YOUTHS AND WOMEN IN IBADAN NORTH EAST AND SOUTH EAST FED. CONSTITTUENCY	25,000,000	NOT DONE	PROJECT NOT YET IMPLEMENTED

MINISTRY	AGENCY	PROJECT TITLES	AMOUNT	STATUS	OBSERVATION
LABOUR	LABOUR	EMPOWERMENT AND TRAINING OF YOUTHS ON FISH AND PROVISION OF STARTER PACKS IN IBARAPA CENTRAL/NORTH	35,700,000	COMPLETED	PROJECT IMPLEMENTED
EDUCATION	UBEC	CONSTRUCTION OF ONE BLOCK OF THREE CLASSROOMS WITH FURNITURE-VOCATIONAL AND ENTREPRENEURSHIP CENTRE,OKAKA (FEDERAL COLLEGE OF ANIMAL HEALTH AND PRODUCTION) - ITESIWAJU LGA	15,000,000	NOT DONE	CONSTRUCTION MADE IN ISOLATED AREA ALONG ISEYIN-SAKI ROAD; SCHOOL ERECTED BUT ESSENTIAL FURNISHINGS, WIRING AND PAINTING STILL LACKING
COMMUNICATIONS	NITDA	PROVISION AND INSTALLATION OF ICT CENTRE IN COMPUTER COLLEGE,OKAKA, ITESIWAJU LGA	20,000,000	COMPLETED	THE ICT CENTER WAS INSTALLED IN OKAKA COMMUNITY GRAMMAR SCHOOL, NOT COMPUTER COLLEGE
POWER	REA	POWER IMPROVEMENT FROM NAVY SCHOOL,IRESAAPA TO IDI- OPELE AND IRANYIN TOWNSHIP ALL IN SURULERE LGA	30,000,000	ONGOING	IDI-OPELE COMMUNITY MEMBERS COMPLAINED THAT ELECTRIC FLAGS AND POLES WERE FIXED TO CAMOUFLAGE NON-IMPLEMENTATION OF PROJECT; THEY HAVE NEVER HAD ELECTRICITY. IN IRANYI TOWNSHIP; NO TRACE OF ELECTRIC POLES OR WIRES REPORTED.
WATER	OORBDA	PROVISION FOR BAJAAS MOTORCYCLES FOR FARMERS IN OGO- OLUWA/SURULERE FEDERAL CONSTITUENCY	6,000,000	NOT DONE	TESTIMONY FROM RESIDENTS IS THAT PROJECT MATERIALS WERE NOT DISTRIBUTED TO FARMERS BUT TO MEMBERS OF THE RULING POLITICAL PARTY
WATER	LNRBDA	PROVISION OF ONE (1) COMPLETE NEW BOREHOLE DRILLING MACHINE IN IBADAN SOUTH-WEST / NORTH- WEST FEDERAL CONSTITUENCY	36,000,000	NOT DONE	PROJECT HAS NOT BEEN IMPLEMENTED
TRADE	TRADE	DATA BASE DEVELOPMENT AND MANAGEMENT IN OGBOMOSHO NORTH/SOUTH/ ORIRE LGAs	35,000,000	NOT DONE	PROJECT HAS NOT BEEN IMPLEMENTED
CULTURE	MAIN MINISTRY	EQUIPMENT,FURNITURE AND ICT FOR MUSEUM AT OTU,ITESIWAJU LGA	100,000,000	COMPLETED	PROJECT COMPLETED BUT ENTIRE OTU COMMUNITY REPORTS THEY HAVE NO ACCESS TO IT YET
CULTURE	MAIN MINISTRY	REHABILITATION OF OTU-IPAPO ROAD,ITESIWAJU LGA	50,000,000	COMPLETED	PROJECT IMPLEMENTED BUT NOT UP TO STANDARD

COMMON CHALLENGES OF THE 2015 CONSTITUENCY PROJECTS

1. Contract Inflation

Inflated costs and pricing of government projects is one of the leading causes of underdevelopment in Nigeria. The unusual cost of construction in the country compared to its peers worldwide is mind-boggling, thereby making contractors the biggest beneficiaries of developmental projects, rather than the people.

2. Unspecified Project Locations

For effective project tracking, it is imperative that detailed project locations are included in the budget. In a lot of instances, location was a missing detail; where communities, civil society and auditing bodies are unaware of a project's location, they are deprived of the opportunity to monitor and ensure proper implementation.

3. Supply of Equipment/Materials to Uncompleted Structures

With little attention to constituency project implementation and monitoring, contractors easily lie to government officials about projects' status in order to access their payment. We have seen instances where a fresh contract is subsequently awarded for the equipment of buildings which when tracked, are proven as uninhabited and uninhabitable.

4. Use of Substandard Products

Severally, government projects are executed with inferior products which consequently causes the loss of lives, developmental setbacks, and attracts more repair and remediation costs for the government. This practice stems from contractors aiming to maximise profit by trimming the cost of implementation or political influence being exerted by the representative(s) of the particular area solely for personal financial gain. At a huge cost to taxpayers, these substandard materials are procured at outrageous prices, with no sanctions from the government when consequences and complaints arise.

5. Non-execution of Projects

Based on the research conducted by the PTO's across the States, many projects were signed off and contractors were paid, with little or no follow-up reporting and assessment by government authorities. A corollary effect is that citizens are often restricted from asking questions, due to the absence of information on project stipulations and status.

6. Lack of an effective Monitoring & Evaluation body to verify Project Implementation and Standards

Budget or project tracking is a vital aspect of the budget implementation process. Effective monitoring of awarded projects eliminates the opportunity for corruption; the use of substandard products; ensures the durability of project structures; enhances citizens' trust in government and also safeguards innocent lives from untimely death and needless injury. The duty of the Ministry of Budget and Planning is to ensure that there is an expedient implementation of the budget for efficient service delivery.

7. Citizens pay to access empowerment, Fertilizers and Skill Acquisition Programs

In certain cases, empowerment programmes earmarked as free for communities in the budget are either rendered as a paid service to constituents, or used to garner political patronage.

8. Citizens are not aware of the budgetary provisions Secrecy in the preparation, enactment, and implementation of the budget, as well as a pervasive lack of transparency conspires to keep citizens in the dark as to what their government owes them.

One of the challenges to development is the lack of access to information about projects in communities. Public projects such as the construction of rural roads, schools, clinics and religious houses are often phrased in technical jargon, making it difficult for citizens to comprehend the budgetary information.

9. Under- implementation of Projects

Certain projects in the budget are brazenly not executed as specified in the budget. There are several instances where the actual work done does not match the description of the budget provision. An example, is the N20 million Construction of 2 unit of two (2) block of three (3) classrooms at Dakata and Tudun Murtala wards in Nassarawa LGA Kano State, where only 1 block of 2 classrooms was constructed, despite an awareness of the authorities that this project was being tracked.

STATE-SPECIFIC RECOMMENDATIONS

In tracking 436 projects so far across 16 States from February to May 2016, we highlight a few trends noted in the field that have wider consequences and lessons and advocate for the following:

Delta and Jigawa - Strategic allocation of funds is crucial

As Nigeria operates its largest budget deficit in at least three decades, the allocation of funds to public projects should remain cost-effective, with sustainability an overriding factor. In Delta State N25 million was budgeted for the renovation of a school hostel in this case, officials should have put more thought into how much it would instead cost to build a new one, while minimising the scope of renovations that call for such a significant expenditure of public funds. To the north, in Jigawa State, the fencing alone of a primary health-care facility cost N20 million; which begs the question: how much would it then cost to build a standard health centre?

Anambra and Cross River - The design of empowerment programmes calls for deeper thought

It is common practice for substantial amounts of money to be allocated to hand-outs of vehicles and machinery under the umbrella term of “empowerment programme.” There is however a need for further deliberation on the procurement and disbursement of such items.

We note the procurement of 13 pieces of Kia Saloon Car for Women Empowerment in Anaocha LGA, Anambra State at a cumulative cost of N65 million, as cars cannot automatically guaranteed empowerment and the sum of N65mn for 13 women is not cost effective. Therefore, projects such as these do not have a direct impact on the women in Anaocha LGA and by their very nature are also highly prone to fraud as disbursement is at the discretion of officials.

In Cross River, more unfortunate and instructive is the Provision of 50 Tricycles for Empowerment of 50 Youths in Calabar South/Bakassi/Akpabuyo Federal Constituency project, worth N32.5 million. In this instance, tricycles were stored in the home of a representative, depreciating all the while and serving no purpose to the people.

It is in the best interest of Nigeria and Nigerians that the government should consider tangibly supporting small-scale business and women entrepreneurs in the community, to enable collective and socially inclusive growth.

Edo and Gombe - Misplaced priorities continue to decimate impact reach

In Edo, we note that a government official implied that a more pressing need for allocations to a State hospital should be research for experts, rather than horticulture development. We are also of the opinion that an enormous sum of N25 million for the

beautification of a clinic is a waste of public resources and should be discouraged in subsequent budgets. This case reiterates the need for constituents to be made a part of all Needs Assessments exercises and budgeting processes to ensure greater impact of scarce resources.

In April 2016 the Gombe State government said it requires the sum of N16 billion to address erosion problems and other environmental challenges. Yet it operates within a system that allocates a whopping N75mn to “Training Research and Development” in Yamaltu/Deba Federal Constituency. We continue to reiterate our belief that bogus terms such as research and development often encourage the embezzlement of public funds, to the detriment of government’s capacity to tackle real problems.

Kebbi - Wilful sabotage of capital projects must be checked, and punished

In Sakaba LGA, a project listed as the provision of N10 million in to farmers was instead converted into loans.

The farmers who received NPK fertilizers report that upon receipt, they are required to pay a sum of N6,000 from the next harvests. Who receives this payment? Is this a new means of generating IGR for the State or are these merely corrupt officials drawing profits off the back of a constituency project?

We submit that if this administration is keen about diversifying the economy, it must support local farmers across the country with inputs and materials to boost production, and plug any loopholes through which corrupt officials sabotage the benefits that should accrue to the people.

Kogi and Niger - Project sustainability and maintenance is key

We note that unless a culture of utilisation of quality materials and maintenance is upheld, line items will remain recurrent and fail to serve the people. In particular we note the Solar Powered Borehole in Ijah Gbah, Niger State which cost N10 million but “didn’t even work up to one month,” as noted by a respondent.

There is also the Rehabilitation of broken down borehole in some locations in Okene LGA, Kogi State, valued at N20 million which was not implemented, with residents stating with pitiful resignation that agitating for service delivery was of no use, as most of the boreholes are out of order after 2 to 3 months of installation.

Niger, Ondo and Gombe - Inadequate execution just as bad as non-execution

In the Niger East Senatorial District, there was a N40 million provision for 20 hand pump boreholes at N2 million for towns in the district. General descriptions like this should be avoided, to enable citizens track projects in their communities and accord respect for due process to governance. A wilful obfuscation of budget details is just as

inimical to development as non-implementation, and it shows a lack of regard for the taxpayers and voters who put their leaders in power.

Another instance of how citizens are shortchanged was witnessed in the “Construction of Clinic at Garafini, Borgu LGA” project, which cost N3.60mn. Although completed, this facility has only two beds, which is undoubtedly unable to offer much succour to the hundreds that live in the community.

The most disheartening consequence of subpar governance is seen in Ondo State, where a N5.5mn project for the Renovation of L.A Primary School, Olorunredo, Ward 4, in Ondo West Senatorial district was so delayed that pupils were seen heading to farms during school hours, as learning was virtually impossible, given the condition of the school.

This should be a wake-up call on the devastating effects of allowing representatives who shirk their legal and legislative responsibilities continue to represent the people. In turn, should the people persistently remain discouraged from exerting their right to demand delivery of capital projects, Nigeria would have effectively mortgaged her future and perpetuated the suffering that threatens a vast majority of her people.

The tracking of projects in this report is supported by the Omidyar Network , Open Society Initiative for West Africa (OSIWA), Making All Voices Count (MAVC) and the United Nations Democracy Fund (UNDEF).

Lead Partner: Oluseun Onigbinde

Tracka Team: Abiola Sosami, Oluwafunso Oladapo and Uadamen Ilevbaoje

Editor: Ruona J. Meyer

Contact: 3rd Floor, 13 Hughes Avenue, Alagomeji, Yaba, Lagos, Nigeria.

Disclaimer: This document has been produced by BudgIT to provide information on budgets and public data issues. BudgIT hereby certifies that all the views expressed in this document accurately reflect our analytical views which we release into the public domain based on empirical evidence and our standards of professionalism. Whilst reasonable care has been taken in preparing this document, no responsibility or liability is accepted for errors or for any views expressed herein by BudgIT or for actions taken as a result of information provided in this Report.

RECOMMENDATIONS

In summary, we respectfully recommend the following to all stakeholders at local, State and federal government levels, as well as policy makers at MDA level:

Citizen Engagement

Representatives should engage their constituents in the budget-making process to ensure their needs are captured in every annual fiscal plan. The fundamental purpose of constituency projects is to ensure rural communities feel the impact of the Federal Government therefore their priorities should be reflected in the budget.

Standardized Platforms for Public Procurement

The Federal government could build a price-check platform on projects to compare initial projects with new projects of identical characteristics. This would assist government in trimming costs, block holes on price inflation and set price guides for contracts.

Effective Budget Monitoring

To achieve an inclusive growth for States, the Federal Government must enforce an effective budget Monitoring and Evaluation body to track project progress and standardise verification. Government could also adopt an independent reporting mechanism for capital projects, to monitor their progress and ensure judicious use of public funds in creating value for the people.

Full implementation of projects

Abandoned projects form a massive leak to public resources the government must strive for full implementation in each State before embarking on new capital projects.

Proper budgeting with relevant information

Project locations should be included in the budget, for easy access by citizens and organisations. As noted, in several cases, budget line items identify project titles, specifications and amounts but fail to establish the actual project site. Provisions like these are extremely prone to misappropriation of funds and corruption.

Open contracting

This must be prioritised, to ensure public participation in contract award with details of all contracts (contractor' name, government budget benchmark, terms of the agreement, bill of quantity, etc) available in the public domain. Government can control incompetence a contract fraud through this initiative via the provision of updated contract information.

Misrepresentation of projects

Public Officials should desist from tagging supply materials in their names for personal glory and political clout citizens should be aware of the actual sponsor of the project - the Federal Government, as enabled by taxpayers.

